


ID	% Complete	Node	Projects	Task Name	Duration	Start	Finish	Predecessors	b	11 April	21 Octob	01 May	11 Nove	21 May	01 Dece	11 June
1	77%			<b>Gate 3 Programme</b>	<b>741 days</b>	<b>Tue 15/07/08</b>	<b>Mon 18/07/11</b>									
2	85%			<b>CER</b>	<b>538 days</b>	<b>Thu 13/11/08</b>	<b>Mon 31/01/11</b>									
3	100%			CER Proposed Direction	0 days	Thu 13/11/08	Thu 13/11/08									
4	100%			CER Final Direction	0 days	Tue 16/12/08	Tue 16/12/08									
5	100%			CER confirm what conventional units and non GPA to add to ITC model and how to include them. Also w	0 days	Fri 16/01/09	Fri 16/01/09									
6	100%			Confirmation of final list of applications and MECs	11 days	Fri 19/12/08	Fri 16/01/09	4								
7	100%			Confirm transmission standard costs and lead times	64 days	Fri 30/01/09	Fri 01/05/09									
8	100%			Proposed Treatment of Conventional Applications	81 days	Wed 01/04/09	Fri 24/07/09	4								
9	100%			Final Direction on treatment of Conventional Applications	103 days	Mon 27/07/09	Fri 18/12/09	8								
10	100%			Treatment of Renewable, Small and Low Carbon Generators outside the GPA	132 days	Mon 19/01/09	Fri 24/07/09									
11	100%			Connection Policy	147 days	Mon 05/01/09	Fri 31/07/09									
12	81%			<b>All-Island dispatch and scheduling</b>	<b>511 days</b>	<b>Mon 05/01/09</b>	<b>Mon 31/01/11</b>									
13	100%			Initial Consultation Paper	130 days	Mon 05/01/09	Wed 08/07/09									
14	100%			Proposed Position Paper	284 days	Thu 09/07/09	Thu 02/09/10									
15	0%			Final Position Paper	97 days	Fri 03/09/10	Mon 31/01/11	14								
16	100%			<b>Joint Pricing Principles and Losses Paper</b>	<b>258 days</b>	<b>Mon 01/06/09</b>	<b>Thu 17/06/10</b>									
17	100%			Decision Paper on Joint Pricing Principles	258 days	Mon 01/06/09	Thu 17/06/10									
18	100%			Losses policy for distribution connected generators	163 days	Mon 01/06/09	Fri 29/01/10									
19	100%			<b>Contracts Process</b>	<b>261 days</b>	<b>Mon 31/08/09</b>	<b>Tue 21/09/10</b>									
20	100%			DSO Standard Connection Agreement	78 days	Mon 31/08/09	Thu 17/12/09									
21	100%			Decision on the process for fixed contracts approach	261 days	Mon 31/08/09	Tue 21/09/10									
22	0%			<b>Decision on TLAFs methodology</b>	<b>206 days</b>	<b>Fri 27/11/09</b>	<b>Fri 01/10/10</b>									
23	100%			<b>Review Firm Access Results</b>	<b>89 days</b>	<b>Fri 11/09/09</b>	<b>Thu 28/01/10</b>									
24	100%			2010-2013	10 days	Fri 11/09/09	Thu 24/09/09									
25	100%			2014-2017	10 days	Fri 04/12/09	Thu 17/12/09									
26	100%			2018-2021	4 days	Fri 15/01/10	Wed 20/01/10									
27	100%			2022-2025	4 days	Mon 25/01/10	Thu 28/01/10									
28	73%			<b>DSO</b>	<b>673 days</b>	<b>Thu 16/10/08</b>	<b>Fri 15/07/11</b>									
29	100%			<b>Produce Shallow Connections</b>	<b>408 days</b>	<b>Wed 21/01/09</b>	<b>Fri 10/09/10</b>	4,140								
30	100%			Area K	135 days	Wed 21/01/09	Fri 31/07/09									
31	100%			Area D	178 days	Wed 21/01/09	Thu 01/10/09									
32	100%			Area H2	152 days	Tue 05/05/09	Fri 04/12/09									
33	100%			Area H1	187 days	Mon 02/03/09	Tue 24/11/09									
34	100%			Area B	195 days	Mon 09/02/09	Fri 13/11/09									
35	100%			Area E	283 days	Wed 21/01/09	Fri 12/03/10									
36	100%			Area J	156 days	Tue 01/09/09	Fri 23/04/10									
37	100%			Area F	204 days	Mon 08/06/09	Wed 07/04/10									
38	100%			Area A	235 days	Tue 04/08/09	Mon 19/07/10									
39	100%			Area G	153 days	Tue 05/01/10	Thu 12/08/10									
40	100%			Area C	127 days	Mon 01/02/10	Tue 03/08/10									
41	100%			Area I	135 days	Mon 01/03/10	Fri 10/09/10									
42	100%			Initial Connection Leadtimes for Constraints Analysis	0 days	Fri 31/07/09	Fri 31/07/09									
43	100%			<b>DSO Cluster Customer Connection Method Meetings</b>	<b>287 days</b>	<b>Fri 01/05/09</b>	<b>Wed 30/06/10</b>	140								
44	100%			Area K	12 days	Fri 01/05/09	Tue 19/05/09									
45	100%			Area D	13 days	Mon 06/07/09	Wed 22/07/09									
46	100%			Area H2	18 days	Mon 31/08/09	Wed 23/09/09									
47	100%			Area H1	34 days	Mon 20/07/09	Fri 04/09/09									
48	100%			Area B	29 days	Mon 13/07/09	Fri 21/08/09									
49	100%			Area E	118 days	Mon 06/07/09	Fri 18/12/09									
50	100%			Area J	79 days	Mon 12/10/09	Fri 12/02/10									
51	100%			Area F	38 days	Mon 23/11/09	Wed 27/01/10									
52	100%			Area A	133 days	Fri 16/10/09	Mon 10/05/10									
53	100%			Area G	52 days	Mon 22/03/10	Thu 03/06/10									
54	100%			Area C	44 days	Mon 15/03/10	Tue 18/05/10									
55	100%			Area I	42 days	Fri 30/04/10	Wed 30/06/10									
56	64%			<b>Application Fees</b>	<b>289 days</b>	<b>Tue 27/10/09</b>	<b>Fri 07/01/11</b>									
57	100%			Invoice fees for offers due to issue in 2009	4 days	Tue 27/10/09	Fri 30/10/09									
58	100%			Invoice fees for offers due to issue in 2010	5 days	Mon 04/01/10	Fri 08/01/10									

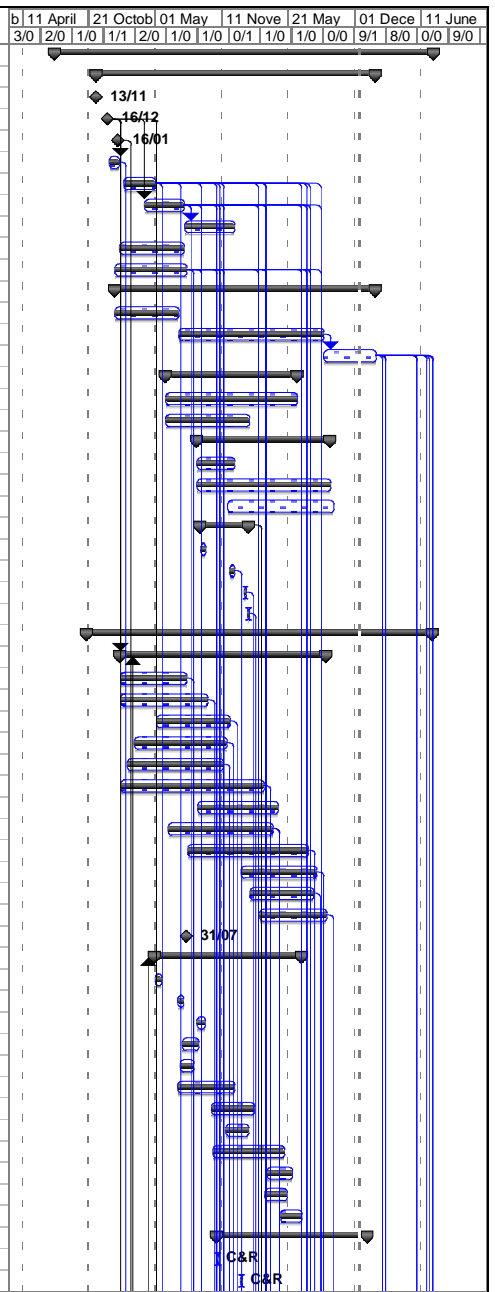


Project: Gate 3 Connection Offer Proces  
Date: Mon 13/12/10

Task Progress Summary External Tasks Split

Split Milestone Project Summary External MileTask

ID	% Complete	Node	Projects	Task Name	Duration	Start	Finish	Predecessors	b	11 April	21 Octob	01 May	11 Nove	21 May	01 Dece	11 June								
									3/0	2/0	1/0	1/1	2/0	1/0	1/0	0/1	1/0	1/0	0/0	9/1	8/0	0/0	9/0	
59	0%			Invoice fees for offers due to issue in 2011	5 days	Mon 03/01/11	Fri 07/01/11																	
60	35%			<b>Issue Offers [CER-08-260]</b>	<b>654 days</b>	<b>Thu 16/10/08</b>	<b>Mon 20/06/11</b>																	
61	100%			Area K	10 days	Mon 14/12/09	Fri 08/01/10																	
62	100%			Area D	10 days	Mon 22/03/10	Fri 02/04/10																	
63	100%			Area H2	11 days	Thu 15/07/10	Thu 29/07/10																	
64	0%			Area H1	16 days	Fri 27/08/10	Fri 17/09/10																	
65	100%			Area B	15 days	Wed 22/09/10	Wed 13/10/10																	
66	100%			Area F	20 days	Wed 27/10/10	Tue 23/11/10	190																
67	0%			Area E	20 days	Tue 08/02/11	Mon 07/03/11																	
68	0%			Area J	15 days	Wed 23/03/11	Wed 13/04/11																	
69	0%			Area A	15 days	Fri 20/05/11	Fri 10/06/11																	
70	0%			Area G	25 days	Thu 16/10/08	Wed 19/11/08																	
71	0%			Area C	15 days	Tue 24/05/11	Tue 14/06/11	204																
72	0%			Area I	14 days	Tue 31/05/11	Mon 20/06/11	207																
73	17%			<b>Issue Offers [CER 10/056]</b>	<b>236 days</b>	<b>Fri 30/07/10</b>	<b>Fri 15/07/11</b>																	
74	100%			<b>Area H2</b>	<b>44 days</b>	<b>Fri 30/07/10</b>	<b>Thu 30/09/10</b>																	
75	100%			Issue Contestable Charges to Distribution Customers	0 days	Fri 30/07/10	Fri 30/07/10																	
76	100%			Sub Group Response	22 days	Fri 30/07/10	Tue 31/08/10	75																
77	100%			Issue Offers	22 days	Wed 01/09/10	Thu 30/09/10	76																
78	27%			<b>Area H1</b>	<b>82 days</b>	<b>Mon 23/08/10</b>	<b>Wed 15/12/10</b>																	
79	100%			Issue Contestable Charges to Distribution Customers (Lisheen)	0 days	Mon 23/08/10	Mon 23/08/10																	
80	100%			Sub Group Response	22 days	Mon 23/08/10	Tue 21/09/10	79																
81	0%			Issue Offers	60 days	Wed 22/09/10	Wed 15/12/10	80																
82	33%			<b>Area H1</b>	<b>54 days</b>	<b>Thu 30/09/10</b>	<b>Wed 15/12/10</b>																	
83	100%			Issue Contestable Charges to Distribution Customers	0 days	Thu 30/09/10	Thu 30/09/10																	
84	80%			Sub Group Response	22 days	Fri 01/10/10	Tue 02/11/10																	
85	0%			Issue Offers	32 days	Tue 02/11/10	Wed 15/12/10																	
86	36%			<b>Area B [West Galway]</b>	<b>114 days</b>	<b>Tue 31/08/10</b>	<b>Fri 18/02/11</b>																	
87	100%			Issue Contestable Charges to Distribution Customers (West Galway)	19 days	Tue 31/08/10	Fri 24/09/10	215																
88	100%			Sub Group Response	22 days	Mon 27/09/10	Wed 27/10/10	87																
89	0%			Issue Offers	73 days	Thu 28/10/10	Fri 18/02/11	88																
90	38%			<b>Area B [Bellacorrick]</b>	<b>89 days</b>	<b>Wed 06/10/10</b>	<b>Fri 18/02/11</b>																	
91	100%			Finalise Charging and Issue to Sub Group	12 days	Wed 06/10/10	Thu 21/10/10	222																
92	100%			Sub Group Response	22 days	Fri 22/10/10	Mon 22/11/10																	
93	0%			Issue Offers	55 days	Tue 23/11/10	Fri 18/02/11	92																
94	0%			<b>Area B</b>	<b>61 days</b>	<b>Mon 15/11/10</b>	<b>Fri 18/02/11</b>																	
95	0%			Finalise Charging and Issue to Sub Group	0 days	Mon 15/11/10	Mon 15/11/10																	
96	0%			Sub Group Response	22 days	Thu 18/11/10	Fri 17/12/10																	
97	0%			Issue Offers	32 days	Thu 06/01/11	Fri 18/02/11	96																
98	0%			<b>Area F</b>	<b>58 days</b>	<b>Tue 30/11/10</b>	<b>Wed 02/03/11</b>																	
99	0%			Finalise Charging and Issue to Sub Group	0 days	Tue 30/11/10	Tue 30/11/10																	
100	0%			Sub Group Response	22 days	Wed 01/12/10	Wed 12/01/11																	
101	0%			Issue Offers	35 days	Thu 13/01/11	Wed 02/03/11	100																
102	0%			<b>Area E</b>	<b>73 days</b>	<b>Mon 14/02/11</b>	<b>Mon 30/05/11</b>																	
103	0%			Finalise Charging and Issue to Sub Group	0 days	Mon 14/02/11	Mon 14/02/11																	
104	0%			Sub Group Response	22 days	Tue 15/02/11	Wed 16/03/11																	
105	0%			Issue Offers	50 days	Fri 18/03/11	Mon 30/05/11	104																
106	26%			<b>Area E (TSO)</b>	<b>159 days</b>	<b>Wed 06/10/10</b>	<b>Wed 01/06/11</b>																	
107	100%			Finalise Charging and Issue to Sub Group ( Kilgarvan)	19 days	Wed 06/10/10	Mon 01/11/10	229																
108	100%			Sub Group Response	22 days	Tue 02/11/10	Wed 01/12/10	107																
109	0%			Issue Offers	118 days	Thu 02/12/10	Wed 01/06/11	108																
110	0%			<b>Area A (TSO)</b>	<b>140 days</b>	<b>Mon 29/11/10</b>	<b>Wed 29/06/11</b>																	
111	0%			Finalise Charging and Issue to Sub Group (Meenadreen)	20 days	Mon 29/11/10	Thu 06/01/11	235																
112	0%			Sub Group Response	22 days	Fri 07/01/11	Mon 07/02/11	111																
113	0%			Issue Offers	100 days	Fri 04/02/11	Wed 29/06/11																	
114	0%			<b>Area A</b>	<b>72 days</b>	<b>Wed 16/03/11</b>	<b>Wed 29/06/11</b>																	
115	0%			Finalise Charging and Issue to Sub Group	0 days	Wed 16/03/11	Wed 16/03/11																	
116	0%			Sub Group Response	22 days	Fri 18/03/11	Tue 19/04/11																	

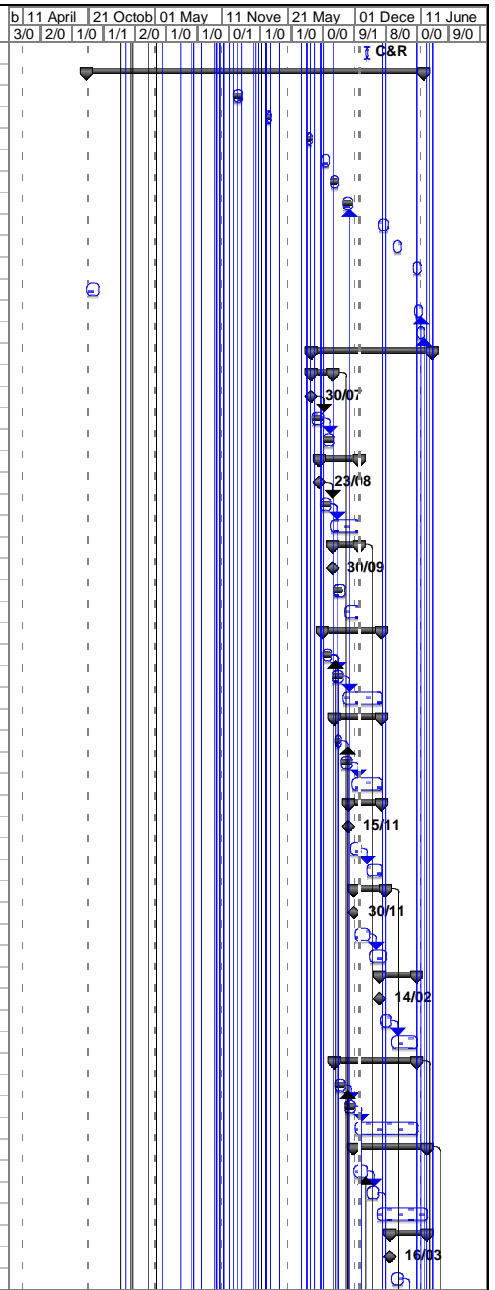


Project: Gate 3 Connection Offer Process Date: Mon 13/12/10

Task: [Patterned bar] Progress: [Solid bar] Summary: [Dashed bar] External Tasks: [Grey bar] Split: [Down arrow]

Split: [Dotted bar] Milestone: [Diamond] Project Summary: [Dashed bar] External MileTask: [Diamond]

ID	% Complete	Node	Projects	Task Name	Duration	Start	Finish	Predecessors	11 April	21 Octob	01 May	11 Nov	21 May	01 Dec	11 June
									3/0	2/0	1/0	1/1	2/0	1/0	1/0
117	0%			Issue Offers	49 days	Wed 20/04/11	Wed 29/06/11	116							
118	0%			<b>Area J</b>	<b>73 days</b>	<b>Mon 14/02/11</b>	<b>Mon 30/05/11</b>								
119	0%			Finalise Charging and Issue to Sub Group	0 days	Mon 14/02/11	Mon 14/02/11								
120	0%			Sub Group Response	22 days	Tue 15/02/11	Wed 16/03/11								
121	0%			Issue Offers	50 days	Fri 18/03/11	Mon 30/05/11	120							
122	0%			<b>Area C</b>	<b>67 days</b>	<b>Thu 31/03/11</b>	<b>Wed 06/07/11</b>								
123	0%			Finalise Charging and Issue to Sub Group	0 days	Thu 31/03/11	Thu 31/03/11								
124	0%			Sub Group Response	22 days	Thu 31/03/11	Tue 03/05/11	123							
125	0%			Issue Offers	45 days	Wed 04/05/11	Wed 06/07/11	124							
126	0%			<b>Area G</b>	<b>53 days</b>	<b>Fri 29/04/11</b>	<b>Thu 14/07/11</b>								
127	0%			Finalise Charging and Issue to Sub Group	0 days	Fri 29/04/11	Fri 29/04/11								
128	0%			Sub Group Response	22 days	Tue 03/05/11	Wed 01/06/11								
129	0%			Issue Offers	30 days	Thu 02/06/11	Thu 14/07/11	128							
130	0%			<b>Area I</b>	<b>44 days</b>	<b>Mon 16/05/11</b>	<b>Fri 15/07/11</b>								
131	0%			Finalise Charging and Issue to Sub Group	0 days	Mon 16/05/11	Mon 16/05/11								
132	0%			Sub Group Response	22 days	Tue 17/05/11	Thu 16/06/11								
133	0%			Issue Offers	22 days	Thu 16/06/11	Fri 15/07/11								
134	77%			<b>TSO</b>	<b>741 days</b>	<b>Tue 15/07/08</b>	<b>Mon 18/07/11</b>								
135	100%			<b>ITC</b>	<b>378 days</b>	<b>Tue 15/07/08</b>	<b>Thu 28/01/10</b>								
136	100%			<b>ITC Preparation</b>	<b>139 days</b>	<b>Tue 15/07/08</b>	<b>Fri 06/02/09</b>								
137	100%			<b>Agree Shallow Connection Nodes</b>	<b>126 days</b>	<b>Tue 15/07/08</b>	<b>Tue 20/01/09</b>								
138	100%			DSO Produce wind database	4.4 wks	Tue 15/07/08	Wed 13/08/08								
139	100%			TSO/DSO agree shallow connection nodes	2 days	Mon 19/01/09	Tue 20/01/09	4,6							
140	100%			Publish shallow connection nodes	0 days	Tue 20/01/09	Tue 20/01/09	139							
141	100%			<b>Prepare and Test ITC Inputs</b>	<b>10 days</b>	<b>Tue 26/01/09</b>	<b>Fri 06/02/09</b>								
142	100%			Finalise ITC Input Files	10 days	Mon 26/01/09	Fri 06/02/09	140,5							
143	100%			<b>ITC Execution</b>	<b>135 days</b>	<b>Mon 06/07/09</b>	<b>Tue 26/01/10</b>								
144	100%			Run ITC from 2010 to 2025	135 days	Mon 06/07/09	Tue 26/01/10								
145	100%			<b>ITC Technical Review</b>	<b>137 days</b>	<b>Mon 06/07/09</b>	<b>Thu 28/01/10</b>								
146	100%			Have review carried out	137 days	Mon 06/07/09	Thu 28/01/10								
147	75%			<b>Offer Process</b>	<b>530 days</b>	<b>Mon 25/05/09</b>	<b>Mon 18/07/11</b>								
148	100%			<b>Application checks</b>	<b>49 days</b>	<b>Mon 07/09/09</b>	<b>Fri 13/11/09</b>								
149	100%			Area B	49 days	Mon 07/09/09	Fri 13/11/09								
150	100%			<b>Initial Connection Method Discussion Meetings</b>	<b>184 days</b>	<b>Mon 25/05/09</b>	<b>Mon 22/02/10</b>								
151	100%			<b>Introductory Customer Meetings for Transmission Renewables</b>	<b>85 days</b>	<b>Mon 25/05/09</b>	<b>Mon 21/09/09</b>	4,7,139							
152	100%			Area K	1 day	Mon 25/05/09	Mon 25/05/09								
153	100%			Area D	1 day	Tue 02/06/09	Tue 02/06/09								
154	100%			Area H2	1 day	Mon 22/06/09	Mon 22/06/09								
155	100%			Area H1	1 day	Mon 29/06/09	Mon 29/06/09								
156	100%			Area B	1 day	Thu 09/07/09	Thu 09/07/09								
157	100%			Area E	1 day	Mon 27/07/09	Mon 27/07/09								
158	100%			Area J	1 day	Mon 10/08/09	Mon 10/08/09								
159	100%			Area F	1 day	Mon 24/08/09	Mon 24/08/09								
160	100%			Area A	1 day	Mon 31/08/09	Mon 31/08/09								
161	100%			Area G	1 day	Mon 07/09/09	Mon 07/09/09								
162	100%			Area C	1 day	Mon 14/09/09	Mon 14/09/09								
163	100%			Area I	1 day	Mon 21/09/09	Mon 21/09/09								
164	100%			Initial Connection Leadtimes for Constraints Analysis	0 days	Fri 10/07/09	Fri 10/07/09								
165	100%			Leadtimes for offers agreed with DSO	17 days	Fri 29/01/10	Mon 22/02/10	23							
166	100%			<b>Publish Offer Leadtimes and Firm Access Quantities</b>	<b>20 days</b>	<b>Fri 18/12/09</b>	<b>Fri 29/01/10</b>								
167	100%			2010-2017	0 days	Fri 18/12/09	Fri 18/12/09	25							
168	100%			2018-2021	0 days	Wed 20/01/10	Wed 20/01/10	26							
169	100%			2021-2025	0 days	Fri 29/01/10	Fri 29/01/10	27							
170	67%			<b>Application Fees</b>	<b>295 days</b>	<b>Fri 16/10/09</b>	<b>Fri 07/01/11</b>								
171	100%			Invoice fees for offers due to issue in 2009	5 days	Fri 16/10/09	Thu 22/10/09								
172	100%			Invoice fees for offers due to issue in 2010	5 days	Mon 04/01/10	Fri 08/01/10								
173	0%			Invoice fees for offers due to issue in 2011	5 days	Mon 03/01/11	Fri 07/01/11								
174	78%			<b>Prepare and Issue Offers [CER-08-260]</b>	<b>458 days</b>	<b>Tue 04/08/09</b>	<b>Thu 16/06/11</b>								

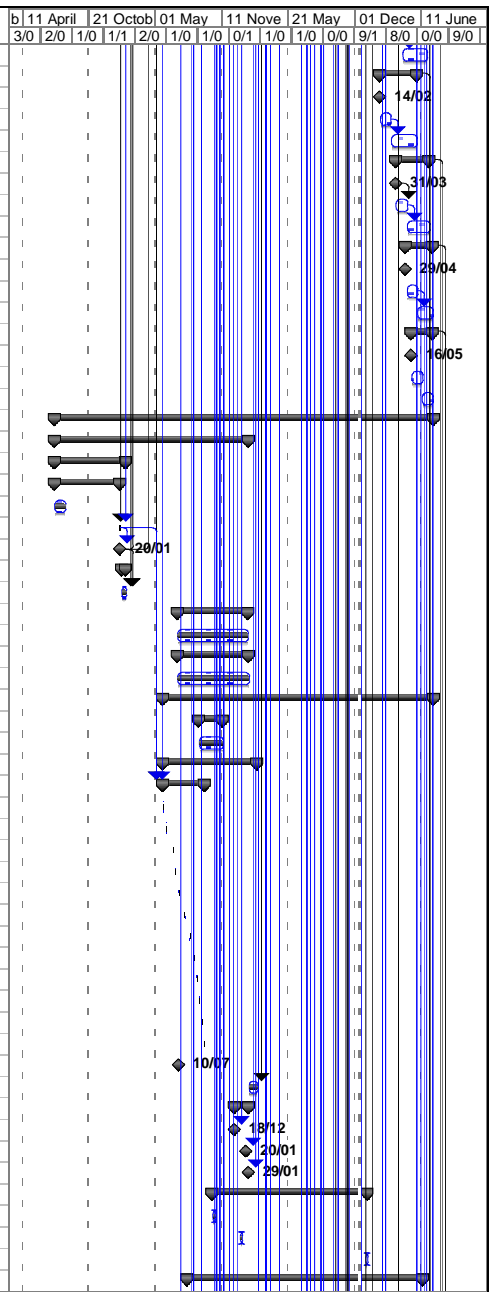

Project: Gate 3 Connection Offer Proces  
Date: Mon 13/12/10

Task Progress Summary External Tasks Split


Split Milestone Project Summary External MileTask

ID	% Complete	Node	Projects	Task Name	Duration	Start	Finish	Predecessors	b	11 April	21 Octob	01 May	11 Nove	21 May	01 Dece	11 June						
									3/0	2/0	1/0	1/1	2/0	1/0	1/0	1/0	0/0	9/1	8/0	0/0	9/0	
175	100%			Area K	82 days	Tue 04/08/09	Thu 26/11/09	8,30,7,11														
176	100%			DSO	82 days	Tue 04/08/09	Thu 26/11/09															
177	100%			TSO	81 days	Tue 04/08/09	Wed 25/11/09															
178	100%			Area D	99 days	Fri 02/10/09	Thu 04/03/10	7,8,11,31														
179	100%			DSO	99 days	Fri 02/10/09	Thu 04/03/10															
180	100%			Area H2	155 days	Mon 07/12/09	Thu 29/07/10	7,8,11,32														
181	100%			DSO	130 days	Mon 07/12/09	Thu 24/06/10															
182	100%			TSO	155 days	Mon 07/12/09	Thu 29/07/10															
183	100%			Area H1	198 days	Wed 25/11/09	Fri 17/09/10	7,8,11,33														
184	100%			DSO	168 days	Wed 25/11/09	Fri 06/08/10															
185	100%			TSO	198 days	Wed 25/11/09	Fri 17/09/10															
186	100%			Area B	222 days	Mon 16/11/09	Wed 13/10/10	7,8,11,34														
187	100%			DSO	192 days	Mon 16/11/09	Tue 31/08/10															
188	100%			TSO	222 days	Mon 16/11/09	Wed 13/10/10															
189	100%			Area F	160 days	Thu 08/04/10	Tue 23/11/10	7,8,11,37														
190	100%			DSO	140 days	Thu 08/04/10	Tue 26/10/10															
191	100%			TSO	160 days	Thu 08/04/10	Tue 23/11/10															
192	87%			Area E	240 days	Mon 15/03/10	Fri 04/03/11	7,8,11,35														
193	97%			DSO	195 days	Mon 15/03/10	Mon 03/01/11															
194	79%			TSO	240 days	Mon 15/03/10	Fri 04/03/11															
195	74%			Area J	249 days	Thu 08/04/10	Tue 12/04/11	7,8,11,37														
196	79%			DSO	219 days	Thu 08/04/10	Fri 25/02/11															
197	70%			TSO	249 days	Thu 08/04/10	Tue 12/04/11															
198	51%			Area A	218 days	Tue 20/07/10	Thu 09/06/11	7,8,11,38														
199	55%			DSO	188 days	Tue 20/07/10	Tue 26/04/11															
200	47%			TSO	218 days	Tue 20/07/10	Thu 09/06/11															
201	48%			Area G	181 days	Fri 13/08/10	Wed 11/05/11	7,8,11,39														
202	48%			DSO	181 days	Fri 13/08/10	Wed 11/05/11															
203	45%			Area C	213 days	Wed 04/08/10	Thu 16/06/11	7,8,11,40														
204	47%			DSO	196 days	Wed 04/08/10	Mon 23/05/11															
205	44%			TSO	213 days	Wed 04/08/10	Thu 16/06/11															
206	38%			Area I	173 days	Mon 13/09/10	Mon 30/05/11	7,8,11,41														
207	38%			DSO	173 days	Mon 13/09/10	Mon 30/05/11															
208	37%			Prepare and Issue Offers [CER 10/056]	210 days	Fri 23/07/10	Wed 01/06/11															
209	100%			Area H1	59 days	Fri 23/07/10	Fri 15/10/10															
210	100%			Issue Contestable Charges to DSO	0 days	Fri 23/07/10	Fri 23/07/10															
211	100%			Sub Group Reponse on Contestability (Bruckana at Lisheen 110kV Station)	0 days	Tue 21/09/10	Tue 21/09/10	80														
212	100%			Prepare and Issue Offers	17 days	Wed 22/09/10	Fri 15/10/10															
213	100%			DSO	17 days	Wed 22/09/10	Fri 15/10/10	211														
214	67%			Area B [West Galway]	114 days	Tue 31/08/10	Fri 18/02/11															
215	100%			Issue Contestable Charges to DSO (West Galway)	0 days	Tue 31/08/10	Tue 31/08/10															
216	100%			Issue Contestable Charges to Transmission Customers (West Galway)	0 days	Fri 24/09/10	Fri 24/09/10	87														
217	100%			Sub Group Reponse on Contestability	22 days	Mon 27/09/10	Wed 27/10/10	87														
218	60%			Issue Offers	73 days	Thu 28/10/10	Fri 18/02/11															
219	100%			DSO	27 days	Thu 28/10/10	Fri 03/12/10	217														
220	45%			TSO	73 days	Thu 28/10/10	Fri 18/02/11	217														
221	54%			Area B [Bellacorrick]	89 days	Wed 06/10/10	Fri 18/02/11															
222	100%			Issue Contestable Charges to DSO (Bellacorrick)	0 days	Wed 06/10/10	Wed 06/10/10															
223	100%			Issue Contestable Charges to Transmission Cstomers (Bellacorrick)	0 days	Thu 21/10/10	Thu 21/10/10	91														
224	100%			Sub Group Reponse on Contestability (Bellacorrick)	22 days	Fri 22/10/10	Mon 22/11/10	223														
225	41%			Issue Offers	55 days	Tue 23/11/10	Fri 18/02/11															
226	80%			DSO	19 days	Tue 23/11/10	Fri 17/12/10	224														
227	27%			TSO	55 days	Tue 23/11/10	Fri 18/02/11	224														
228	10%			Area E	159 days	Wed 06/10/10	Wed 01/06/11															
229	100%			Issue Contestable Charges to DSO	0 days	Wed 06/10/10	Wed 06/10/10															
230	0%			Sub Group Reponse on Contestability (Area E)	0 days	Wed 01/12/10	Wed 01/12/10	108														
231	10%			Issue Offers	118 days	Thu 02/12/10	Wed 01/06/11															
232	19%			DSO	43 days	Thu 02/12/10	Fri 11/02/11	230														

Project: Gate 3 Connection Offer Proces Date: Mon 13/12/10

Task Split Progress Milestone Summary Project Summary External Tasks External MileTask Split

ID	% Complete	Node	Projects	Task Name	Duration	Start	Finish	Predecessors	b	11 April	21 Octob	01 May	11 Nove	21 May	01 Dece	11 June								
									3/0	2/0	1/0	1/1	2/0	1/0	1/0	0/1	1/0	1/0	0/0	9/1	8/0	0/0	9/0	
233	7%			TSO	118 days	Thu 02/12/10	Wed 01/06/11	230																
234	0%			<b>Area A</b>	<b>98 days</b>	<b>Fri 26/11/10</b>	<b>Thu 28/04/11</b>																	
235	0%			Issue Contestable Charges to DSO	0 days	Fri 26/11/10	Fri 26/11/10																	
236	0%			Sub Group Response on Contestability	0 days	Mon 07/02/11	Mon 07/02/11	112																
237	0%			<b>Issue Offers</b>	<b>56 days</b>	<b>Tue 08/02/11</b>	<b>Thu 28/04/11</b>																	
238	0%			DSO	56 days	Tue 08/02/11	Thu 28/04/11	236																
239	90%			<b>Constraints Information</b>	<b>460 days</b>	<b>Tue 01/09/09</b>	<b>Mon 18/07/11</b>																	
240	100%			Perform Constraint Studies	243 days	Tue 01/09/09	Fri 27/08/10																	
241	99%			<b>PGOR Reports</b>	<b>63 days</b>	<b>Mon 20/09/10</b>	<b>Thu 16/12/10</b>																	
242	100%			Reports Available for Region K	1 day	Mon 20/09/10	Mon 20/09/10																	
243	100%			Reports Available for Region D	1 day	Mon 20/09/10	Mon 20/09/10																	
244	100%			Reports Available for Region H2	1 day	Fri 01/10/10	Fri 01/10/10	74																
245	98%			Reports Available for Area H1	1 day	Thu 16/12/10	Thu 16/12/10	82																
246	0%			<b>Constraint Reports</b>	<b>116 days</b>	<b>Tue 01/02/11</b>	<b>Mon 18/07/11</b>																	
247	0%			Impact Assessment of Scheduling and Dispatch Paper	20 days	Tue 01/02/11	Mon 28/02/11	15																
248	0%			Report Available for Region K, D, H2, H1 & B	1 day	Tue 01/03/11	Tue 01/03/11	15,247																
249	0%			Report Available for Region F	1 day	Thu 03/03/11	Thu 03/03/11	15,98,247																
250	0%			Report Available for Region E	1 day	Thu 02/06/11	Thu 02/06/11	15,106,247																
251	0%			Report Available for Region J	1 day	Tue 31/05/11	Tue 31/05/11	15,118,247																
252	0%			Report Available for Region A	1 day	Thu 30/06/11	Thu 30/06/11	15,110,247																
253	0%			Report Available for Region G	1 day	Fri 15/07/11	Fri 15/07/11	15,126,247																
254	0%			Report Available for Region C	1 day	Thu 07/07/11	Thu 07/07/11	15,122,247																
255	0%			Report Available for Region I	1 day	Mon 18/07/11	Mon 18/07/11	15,130,247																

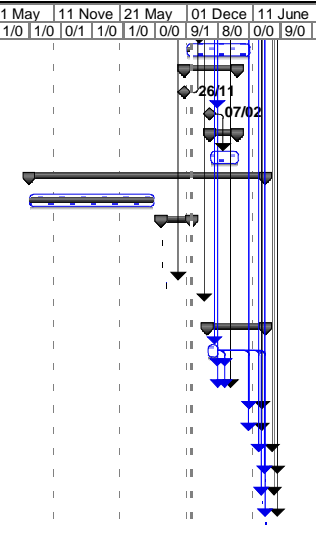

Project: Gate 3 Connection Offer Proces  
Date: Mon 13/12/10

Task Split Progress Milestone Summary Project Summary External Tasks External MileTask Split
