


ID	% Complete	Task Name	Duration	Start	Finish	March		January			November			September	
						M	B	E	M	B	E	M	B		
1	59%	Gate 3 Programme	727 days	Tue 15/07/08	Wed 29/06/11										
2	94%	CER	334 days	Thu 13/11/08	Wed 31/03/10										
3	100%	CER Proposed Direction	0 days	Thu 13/11/08	Thu 13/11/08			◆							
4	100%	CER Final Direction	0 days	Tue 16/12/08	Tue 16/12/08			◆							
5	100%	CER confirm what conventional units and non GPA to add to ITC model and how to include them. Also v	0 days	Fri 16/01/09	Fri 16/01/09			◆							
6	100%	Confirmation of final list of applications and MECs	11 days	Fri 19/12/08	Fri 16/01/09										
7	100%	Confirm transmission standard costs and lead times	64 days	Fri 30/01/09	Fri 01/05/09										
8	100%	Proposed Treatment of Conventional Applications	81 days	Wed 01/04/09	Fri 24/07/09										
9	100%	Final Direction on treatment of Conventional Applications	103 days	Mon 27/07/09	Fri 18/12/09										
10	100%	Treatment of Renewable, Small and Low Carbon Generators outside the GPA	132 days	Mon 19/01/09	Fri 24/07/09										
11	100%	Connection Policy	147 days	Mon 05/01/09	Fri 31/07/09										
12	91%	All-Island dispatch and scheduling	307 days	Mon 05/01/09	Wed 31/03/10										
13	100%	Initial Consultation Paper	130 days	Mon 05/01/09	Wed 08/07/09										
14	85%	Proposed Direction	177 days	Thu 09/07/09	Wed 31/03/10										
15	99%	Joint Pricing Principles and Losses Paper	183 days	Mon 01/06/09	Fri 26/02/10										
16	97%	Approval of Revisions to Joint Pricing Paper or Proposed Direction	183 days	Mon 01/06/09	Fri 26/02/10										
17	100%	Losses policy for distribution connected generators	163 days	Mon 01/06/09	Fri 29/01/10										
18	85%	Contracts Process	141 days	Mon 31/08/09	Wed 31/03/10										
19	100%	DSO Standard Connection Agreement	78 days	Mon 31/08/09	Thu 17/12/09										
20	81%	Process for implementation of the "fixed date with payments" approach	141 days	Mon 31/08/09	Wed 31/03/10										
21	81%	Levels of incentives, payments, margins, etc & other rules re "fixed date with payments" approach	141 days	Mon 31/08/09	Wed 31/03/10										
22	96%	Contestability for Distribution & Transmission Level Connections to the Electricity System	119 days	Mon 31/08/09	Fri 26/02/10										
23	68%	Locational Signals Options, (includes TUoS & TLAFs)	75 days	Fri 27/11/09	Fri 26/03/10										
24	100%	Review Firm Access Results	89 days	Fri 11/09/09	Thu 28/01/10										
25	100%	2010-2013	10 days	Fri 11/09/09	Thu 24/09/09										
26	100%	2014-2017	10 days	Fri 04/12/09	Thu 17/12/09										
27	100%	2018-2021	4 days	Fri 15/01/10	Wed 20/01/10										
28	100%	2022-2025	4 days	Mon 25/01/10	Thu 28/01/10										
29	81%	DSO	647 days	Thu 16/10/08	Fri 10/06/11										
30	89%	Produce Shallow Connections	408 days	Wed 21/01/09	Fri 10/09/10										
31	100%	Area K	135 days	Wed 21/01/09	Fri 31/07/09										
32	100%	Area D	178 days	Wed 21/01/09	Thu 01/10/09										
33	100%	Area H2	152 days	Tue 05/05/09	Fri 04/12/09										
34	100%	Area H1	187 days	Mon 02/03/09	Tue 24/11/09										
35	100%	Area B	195 days	Mon 09/02/09	Fri 13/11/09										
36	100%	Area E	283 days	Wed 21/01/09	Fri 12/03/10										
37	100%	Area J	156 days	Tue 01/09/09	Fri 23/04/10										
38	100%	Area F	204 days	Mon 08/06/09	Wed 07/04/10										
39	65%	Area A	235 days	Tue 04/08/09	Mon 19/07/10										
40	20%	Area G	153 days	Tue 05/01/10	Thu 12/08/10										
41	100%	Area C	127 days	Mon 01/02/10	Tue 03/08/10										
42	80%	Area I	135 days	Mon 01/03/10	Fri 10/09/10										
43	100%	Initial Connection Leadtimes for Constraints Analysis	0 days	Fri 31/07/09	Fri 31/07/09										
44	78%	DSO Cluster Customer Connection Method Meetings	287 days	Fri 01/05/09	Wed 30/06/10										
45	100%	Area K	12 days	Fri 01/05/09	Tue 19/05/09										
46	100%	Area D	13 days	Mon 06/07/09	Wed 22/07/09										
47	100%	Area H2	18 days	Mon 31/08/09	Wed 23/09/09										
48	100%	Area H1	34 days	Mon 20/07/09	Fri 04/09/09										
49	100%	Area B	29 days	Mon 13/07/09	Fri 21/08/09										

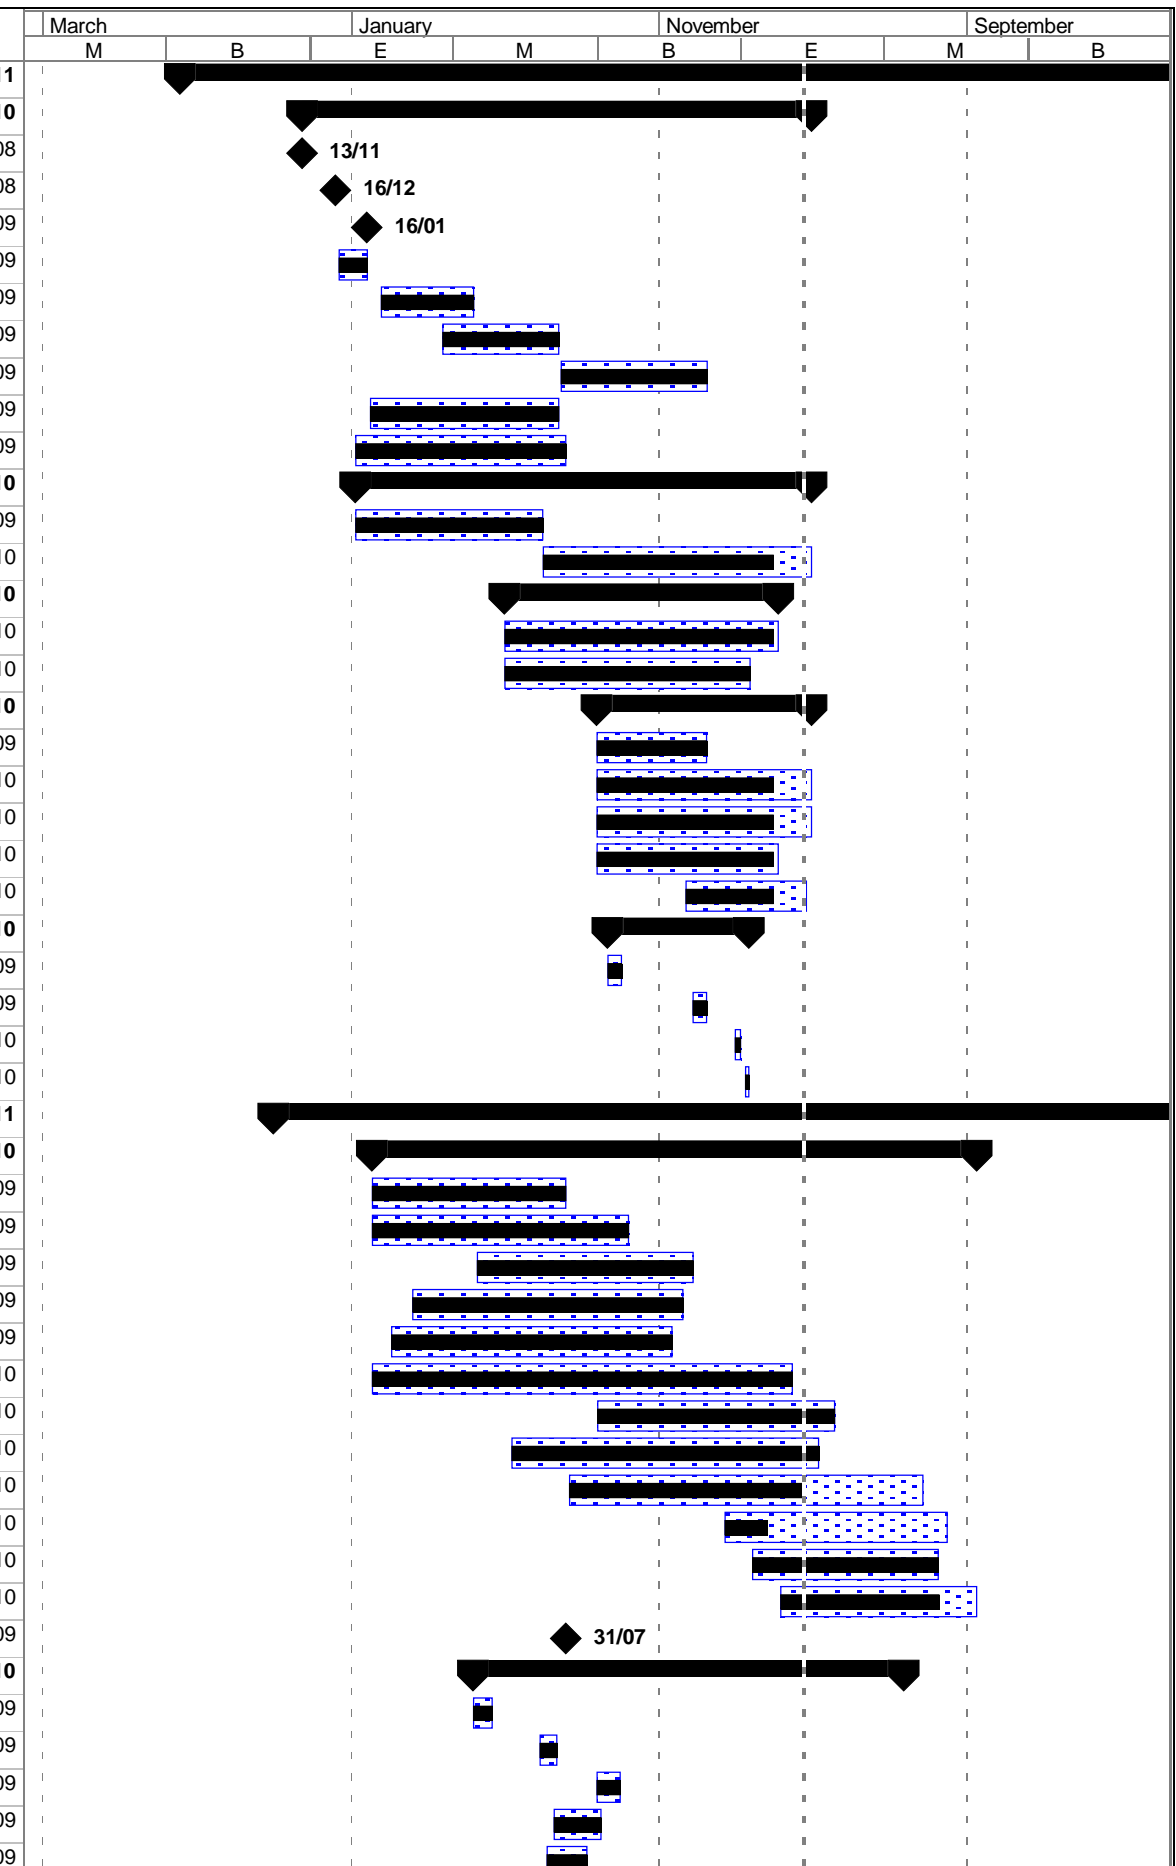


Project: Gate 3 Connection Offer Proce
Date: Tue 23/03/10

Task Progress Summary External Tasks Split

Split Milestone Project Summary External MileTask

ID	% Complete	Task Name	Duration	Start	Finish	March		January		November		September	
						M	B	E	M	B	E	M	B
50	100%	Area E	118 days	Mon 06/07/09	Fri 18/12/09								
51	100%	Area J	79 days	Mon 12/10/09	Fri 12/02/10								
52	100%	Area F	38 days	Mon 23/11/09	Wed 27/01/10								
53	38%	Area A	133 days	Fri 16/10/09	Mon 10/05/10								
54	0%	Area G	52 days	Mon 22/03/10	Thu 03/06/10								
55	100%	Area C	44 days	Mon 15/03/10	Tue 18/05/10								
56	100%	Area I	42 days	Fri 30/04/10	Wed 30/06/10								
57	64%	Application Fees	288 days	Tue 27/10/09	Fri 07/01/11								
58	100%	Invoice fees for offers due to issue in 2009	4 days	Tue 27/10/09	Fri 30/10/09								
59	100%	Invoice fees for offers due to issue in 2010	5 days	Mon 04/01/10	Fri 08/01/10								
60	0%	Invoice fees for offers due to issue in 2011	5 days	Mon 03/01/11	Fri 07/01/11								
61	5%	Issue Offers	647 days	Thu 16/10/08	Fri 10/06/11								
62	100%	Area K	10 days	Mon 14/12/09	Fri 08/01/10								
63	0%	Area D	10 days	Mon 22/03/10	Fri 02/04/10								
64	0%	Area H2	11 days	Thu 15/07/10	Thu 29/07/10								
65	0%	Area H1	16 days	Fri 27/08/10	Fri 17/09/10								
66	0%	Area B	15 days	Wed 22/09/10	Wed 13/10/10								
67	0%	Area F	20 days	Thu 16/10/08	Wed 12/11/08								
68	0%	Area E	20 days	Tue 08/02/11	Mon 07/03/11								
69	0%	Area J	15 days	Wed 23/03/11	Wed 13/04/11								
70	0%	Area A	15 days	Fri 20/05/11	Fri 10/06/11								
71	0%	Area G	25 days	Thu 16/10/08	Wed 19/11/08								
72	0%	Area C	15 days	Thu 16/10/08	Wed 05/11/08								
73	0%	Area I	14 days	Thu 16/10/08	Tue 04/11/08								
74	28%	TSO	727 days	Tue 15/07/08	Wed 29/06/11								
75	100%	ITC	378 days	Tue 15/07/08	Thu 28/01/10								
76	100%	ITC Preparation	139 days	Tue 15/07/08	Fri 06/02/09								
77	100%	Agree Shallow Connection Nodes	126 days	Tue 15/07/08	Tue 20/01/09								
78	100%	DSO Produce wind database	4.4 wks	Tue 15/07/08	Wed 13/08/08								
79	100%	TSO/DSO agree shallow connection nodes	2 days	Mon 19/01/09	Tue 20/01/09								
80	100%	Publish shallow connection nodes	0 days	Tue 20/01/09	Tue 20/01/09								
81	100%	Prepare and Test ITC Inputs	10 days	Mon 26/01/09	Fri 06/02/09								
82	100%	Finalise ITC Input Files	10 days	Mon 26/01/09	Fri 06/02/09								
83	100%	ITC Execution	135 days	Mon 06/07/09	Tue 26/01/10								
84	100%	Run ITC from 2010 to 2025	135 days	Mon 06/07/09	Tue 26/01/10								
85	100%	ITC Technical Review	137 days	Mon 06/07/09	Thu 28/01/10								
86	100%	Have review carried out	137 days	Mon 06/07/09	Thu 28/01/10								
87	23%	Offer Process	660 days	Thu 16/10/08	Wed 29/06/11								
88	100%	Application checks	49 days	Mon 07/09/09	Fri 13/11/09								
89	100%	Area B	49 days	Mon 07/09/09	Fri 13/11/09								
90	100%	Initial Connection Method Discussion Meetings	184 days	Mon 25/05/09	Mon 22/02/10								
91	100%	Introductory Customer Meetings for Transmission Renewables	85 days	Mon 25/05/09	Mon 21/09/09								
92	100%	Area K	1 day	Mon 25/05/09	Mon 25/05/09								
93	100%	Area D	1 day	Tue 02/06/09	Tue 02/06/09								
94	100%	Area H2	1 day	Mon 22/06/09	Mon 22/06/09								
95	100%	Area H1	1 day	Mon 29/06/09	Mon 29/06/09								
96	100%	Area B	1 day	Thu 09/07/09	Thu 09/07/09								
97	100%	Area E	1 day	Mon 27/07/09	Mon 27/07/09								
98	100%	Area J	1 day	Mon 10/08/09	Mon 10/08/09								

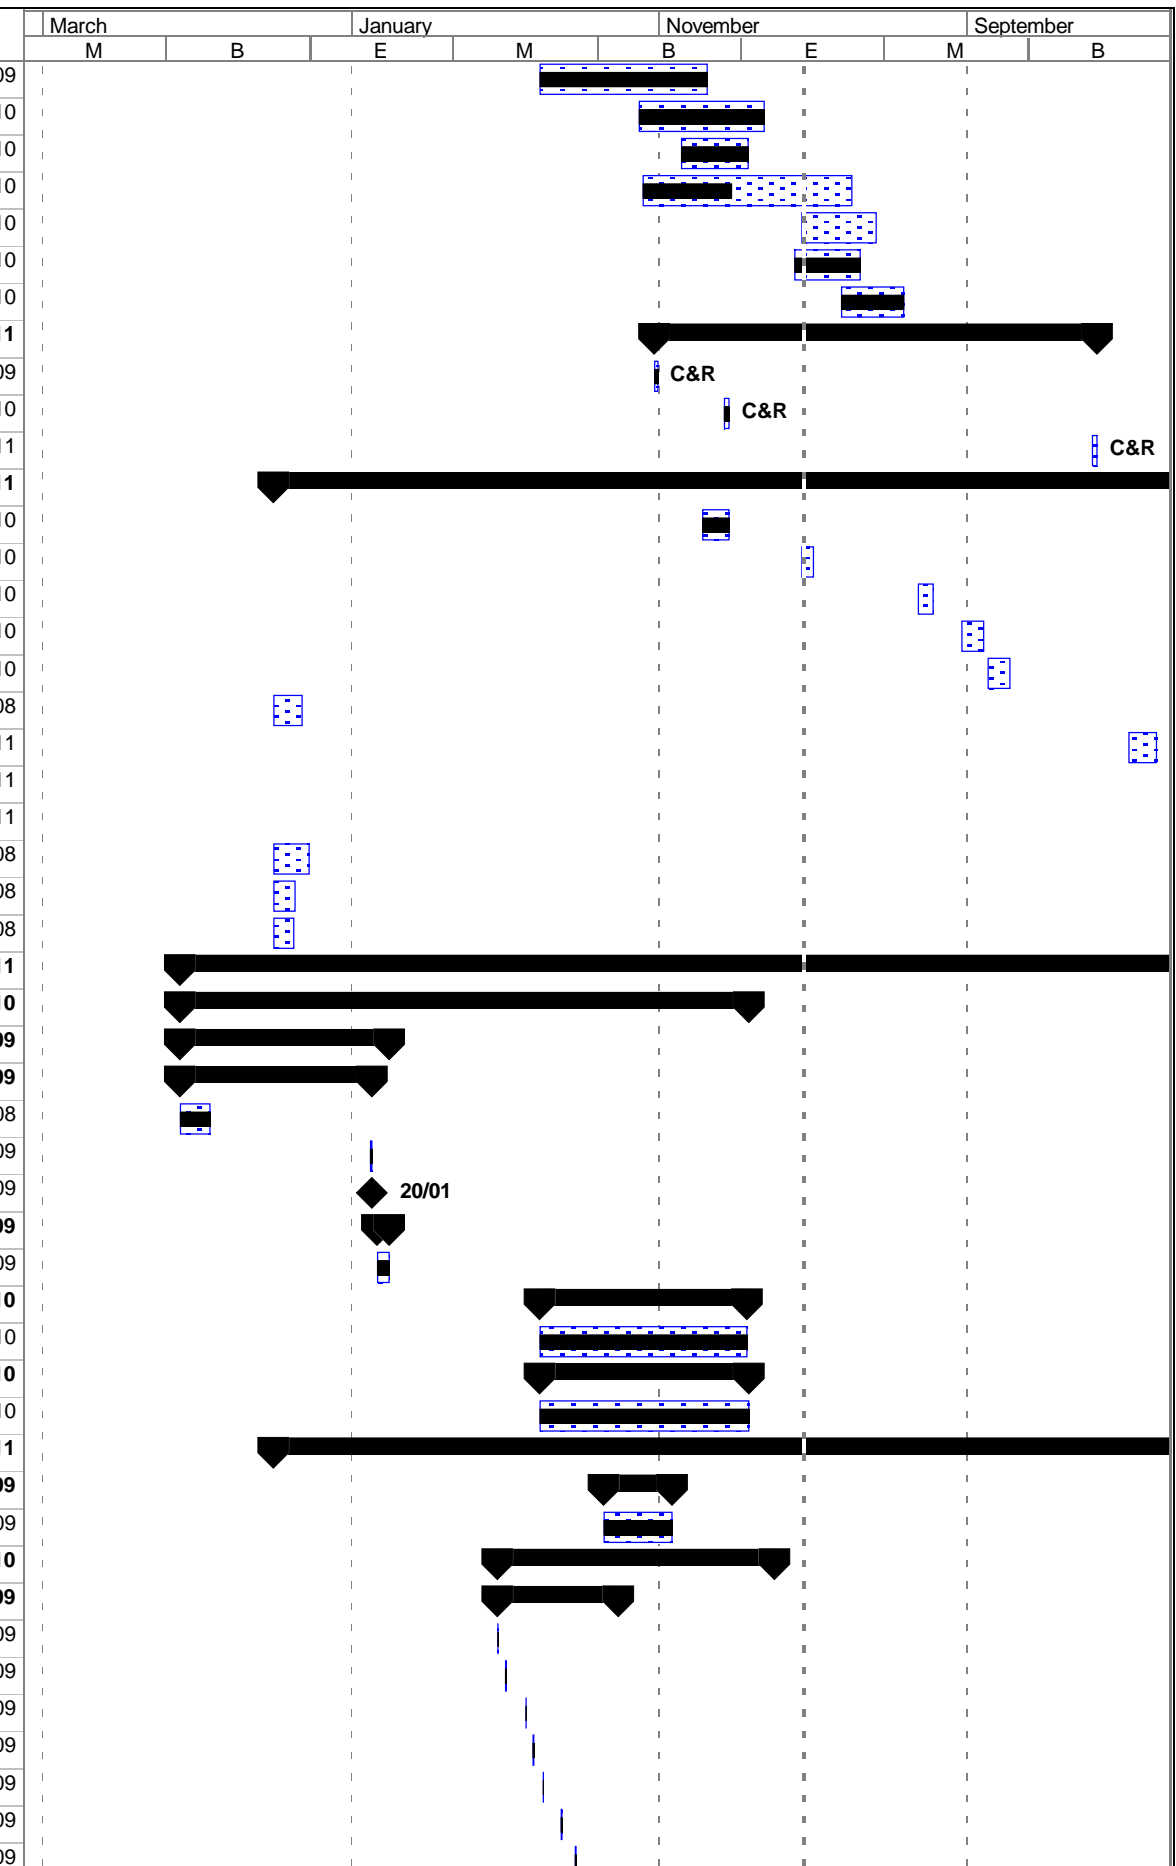






Project: Gate 3 Connection Offer Proce
Date: Tue 23/03/10




Task Progress Summary External Tasks Split

Split Milestone Project Summary External MileTask

ID	% Complete	Task Name	Duration	Start	Finish	March		January		November		September	
						M	B	E	M	B	E	M	B
99	100%	Area F	1 day	Mon 24/08/09	Mon 24/08/09								
100	100%	Area A	1 day	Mon 31/08/09	Mon 31/08/09								
101	100%	Area G	1 day	Mon 07/09/09	Mon 07/09/09								
102	100%	Area C	1 day	Mon 14/09/09	Mon 14/09/09								
103	100%	Area I	1 day	Mon 21/09/09	Mon 21/09/09								
104	100%	Initial Connection Leadtimes for Constraints Analysis	0 days	Fri 10/07/09	Fri 10/07/09								
105	100%	Leadtimes for offers agreed with DSO	17 days	Fri 29/01/10	Mon 22/02/10								
106	100%	Publish Offer Leadtimes and Firm Access Quantities	20 days	Fri 18/12/09	Fri 29/01/10								
107	100%	2010-2017	0 days	Fri 18/12/09	Fri 18/12/09								
108	100%	2018-2021	0 days	Wed 20/01/10	Wed 20/01/10								
109	100%	2021-2025	0 days	Fri 29/01/10	Fri 29/01/10								
110	67%	Application Fees	294 days	Fri 16/10/09	Fri 07/01/11								
111	100%	Invoice fees for offers due to issue in 2009	5 days	Fri 16/10/09	Thu 22/10/09								
112	100%	Invoice fees for offers due to issue in 2010	5 days	Mon 04/01/10	Fri 08/01/10								
113	0%	Invoice fees for offers due to issue in 2011	5 days	Mon 03/01/11	Fri 07/01/11								
114	18%	Prepare and Issue Offers	537 days	Thu 16/10/08	Mon 03/01/11								
115	100%	Area K	82 days	Tue 04/08/09	Thu 26/11/09								
116	100%	DSO	82 days	Tue 04/08/09	Thu 26/11/09								
117	100%	TSO	81 days	Tue 04/08/09	Wed 25/11/09								
118	100%	Area D	99 days	Fri 02/10/09	Thu 04/03/10								
119	100%	DSO	99 days	Fri 02/10/09	Thu 04/03/10								
120	44%	Area H2	155 days	Mon 07/12/09	Thu 29/07/10								
121	48%	DSO	130 days	Mon 07/12/09	Thu 24/06/10								
122	40%	TSO	155 days	Mon 07/12/09	Thu 29/07/10								
123	38%	Area H1	198 days	Wed 25/11/09	Fri 17/09/10								
124	42%	DSO	168 days	Wed 25/11/09	Fri 06/08/10								
125	35%	TSO	198 days	Wed 25/11/09	Fri 17/09/10								
126	37%	Area B	222 days	Mon 16/11/09	Wed 13/10/10								
127	40%	DSO	192 days	Mon 16/11/09	Tue 31/08/10								
128	35%	TSO	222 days	Mon 16/11/09	Wed 13/10/10								
129	0%	Area F	160 days	Thu 16/10/08	Mon 15/06/09								
130	0%	DSO	140 days	Thu 16/10/08	Mon 18/05/09								
131	0%	TSO	160 days	Thu 16/10/08	Mon 15/06/09								
132	0%	Area E	537 days	Thu 16/10/08	Mon 03/01/11								
133	0%	DSO	195 days	Mon 15/03/10	Mon 03/01/11								
134	0%	TSO	240 days	Thu 16/10/08	Tue 06/10/09								
135	0%	Area J	249 days	Thu 16/10/08	Mon 19/10/09								
136	0%	DSO	219 days	Thu 16/10/08	Mon 07/09/09								
137	0%	TSO	249 days	Thu 16/10/08	Mon 19/10/09								
138	0%	Area A	218 days	Thu 16/10/08	Fri 04/09/09								
139	0%	DSO	188 days	Thu 16/10/08	Thu 23/07/09								
140	0%	TSO	218 days	Thu 16/10/08	Fri 04/09/09								
141	0%	Area G	181 days	Thu 16/10/08	Tue 14/07/09								
142	0%	DSO	181 days	Thu 16/10/08	Tue 14/07/09								
143	0%	Area C	213 days	Thu 16/10/08	Fri 28/08/09								
144	0%	DSO	196 days	Thu 16/10/08	Wed 05/08/09								
145	0%	TSO	213 days	Thu 16/10/08	Fri 28/08/09								
146	0%	Area I	173 days	Thu 16/10/08	Thu 02/07/09								
147	0%	DSO	173 days	Thu 16/10/08	Thu 02/07/09								

Project: Gate 3 Connection Offer Proce
Date: Tue 23/03/10

Task  Progress  Summary  External Tasks  Split 

Split  Milestone  Project Summary  External MileTask 
