







Network Delivery Portfolio

366

Reporting Period:

Q1 2024

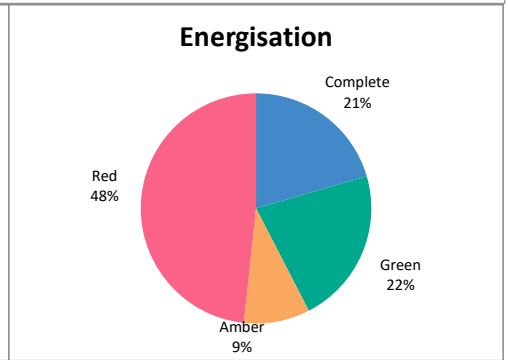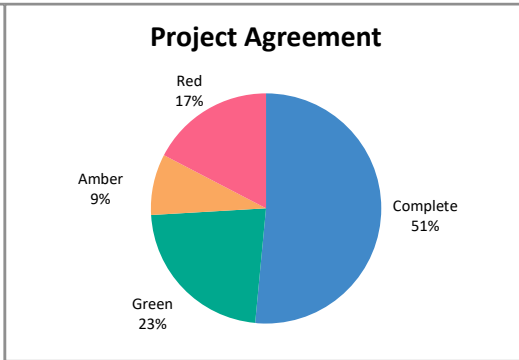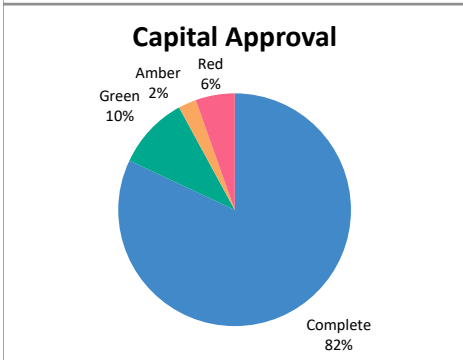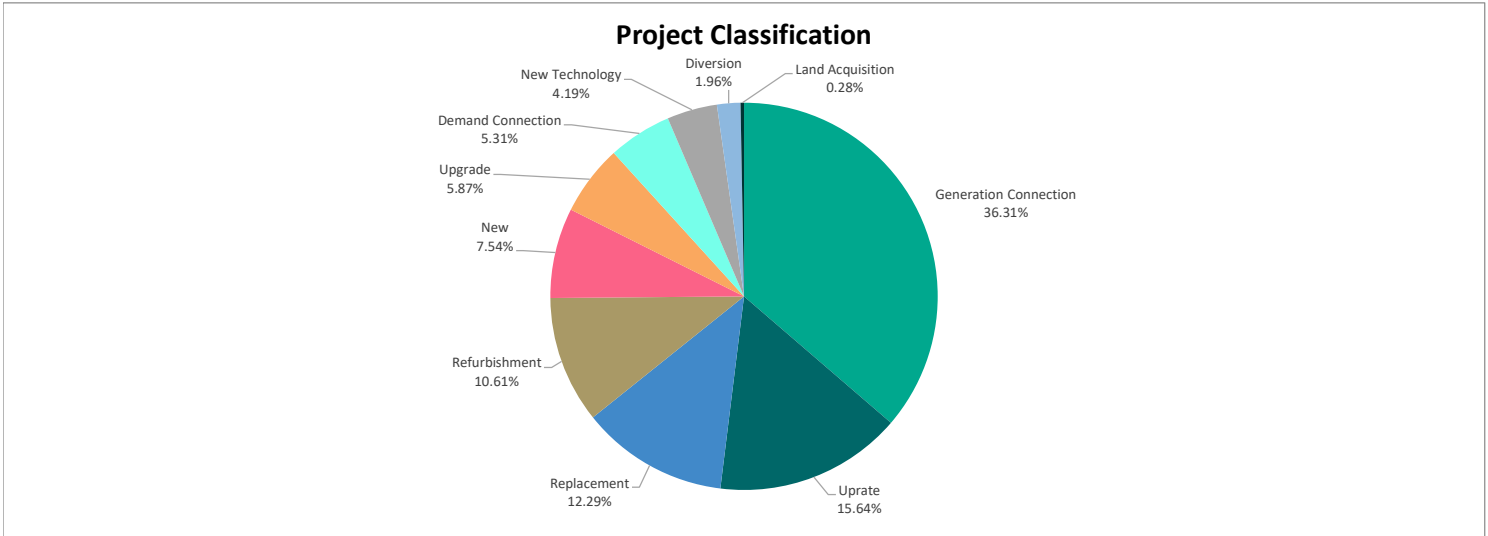

Gateway 3 / Capital Approval (GW3/CA)

Once the grid requirements have been identified and assessed, the project is then approved by submitting the Gateway 3 Paper. At this point, milestone dates for the subsequent gateways are set.

Gateway 6 / Project Agreement (GW6/PA)

This is when the final deliverables of the project are formally agreed and the project is handed over to ESB Networks to deliver the agreed solution.

Energisation (EI)

The Energisation date is when the work is substantially complete, the project has been energised and is ready to transfer power. The energisation of new plant and equipment requires an 'outage' to enable the commissioning teams to work safely.

Disclaimer
 Dates shown in the Network Delivery Portfolio are based on an unconstrained scenario and are, therefore, indicative and subject to change. Information in these documents with reference to completion dates (Energisation (EI) Dates, Estimated Completion Dates, Forecast Completion Dates and Indicative Completion Dates) has been prepared with all reasonable care and diligence.

EirGrid is focused on completing reinforcements which give us most benefit and have the highest degree of deliverability. Customer connection programmes are also subject to change, and we are focused on delivering demand and renewable customer connections which support economic and social development while meeting government targets.

While all reasonable care has been taken to prepare this document, and the accompanying Network Delivery Portfolio (NDP) dataset, we can make no guarantee to the quality, accuracy and completeness of the information herein. We do not accept responsibility for any loss associated with the use of this information. Use of these documents and the information they contain is at the user's own risk. Information in these documents does not amount to a recommendation as regards to any possible investment. Before taking a business decision based on the content of these NDP documents, we advise that interested parties seek separate and independent opinion in relation to the matters covered by these documents.

All outage information is published here: <https://www.eirgridgroup.com/customer-and-industry/general-customer-information/outage-information/>

RAG Status Key

■	Milestone Achieved
■	Milestone Achievable within 3 months of PR5 Baseline
■	Milestone Achievable within 12 months of PR5 Baseline
■	Milestone Achievable outside of 12 months of PR5 Baseline

Footnote:

- * The timeline for this project is currently being updated. Additional information will be provided in the next quarterly update.
- ** Energisation date Not Applicable
- *** Local Security of Supply (LSoS) Incentive Plan Projects

New Projects or changes since last publication

ProjectCode	ProjectName	Latest bg2nd	Latest bg2nd5	Latest bg2nd9
Project Code	Project Name	GW3 (CA)	GW6 (PA)	Energisation (EI)
CP0466	North South 400 kV Interconnector - RoI	21/09/2016	28/06/2024	30/06/2027
CP0501	Clashavoon - Dunmanway 110 kV Line - New Line	12/09/2009	18/12/2013	11/09/2020
CP0580	Carrickmines 220 kV GIS Development	15/12/2007	14/02/2012	10/10/2021
CP0585	Laois Kilkenny (Coolnabacky) 400 kV Station - New Station & Associated Lines & Station Works	16/04/2008	17/06/2016	02/11/2026
CP0622	Tarbert 220 kV Station Upgrade*	29/05/2012	16/12/2014	
CP0624	Killonan 220 kV Station Refurbishment - Killonan Station Works	30/09/2011	01/04/2019	16/11/2027
CP0644	Bracklone 110 kV Station - DSO	19/03/2020	01/06/2022	01/06/2026
CP0646	Finglas 110 kV station redevelopment	28/08/2009	24/08/2012	31/10/2025
CP0647	Kilpaddoge 220-110 kV station	01/07/2009	30/07/2012	30/06/2022
CP0668	Corduff - Ryebrook 110 kV line uprate	29/04/2011	10/05/2013	02/06/2023
CP0692	Inchicore - 220 kV GIS Station Upgrade	21/09/2016	20/03/2019	30/11/2026
CP0693	Baroda 110 kV station - 2 x 110 kV Trafo Bays DSO*	14/06/2019	10/01/2020	30/03/2025
CP0724	Thornsberry 110KV Station Busbar uprate	01/03/2011	07/11/2012	30/11/2023
CP0726	Kilpaddoge - Knockanure 220 kV cable	10/03/2011	16/03/2016	30/06/2022
CP0741	Trabeg 110 kV station - uprate 2 x 110 kV transformer bays and control room extension DSO	03/06/2020	29/04/2021	01/05/2025
CP0749	Offshore Placeholder Project*	27/03/2020	31/12/2024	30/06/2027
CP0763	Clashavoon - Tarbert 220 kV line uprate	21/12/2011	20/03/2015	04/11/2022
CP0771	Castlebar 110 kV station busbar uprate	07/05/2013	25/01/2016	31/08/2022
CP0792	Finglas 220 kV Reconfiguration Project	22/04/2015	11/03/2018	31/10/2025
CP0794	Aghada 220 kV Station Busbar Reconfiguration	21/12/2012	16/12/2014	30/11/2021
CP0796	Knockraha station & installation of additional couplers	21/09/2016	30/09/2016	30/11/2025
CP0799	Louth 220 kV Station Refurbishment*	25/09/2013	12/03/2020	28/02/2029
CP0808	Maynooth 220 kV Station Reconfiguration	16/03/2021	05/12/2024	08/03/2028
CP0813	Trien 110 kV Station Works	04/04/2019	22/10/2021	31/10/2024
CP0816	North Connacht 110 kV Project	12/09/2018	20/12/2023	31/03/2028
CP0817	Flagford - Sliabh Bawn 110 kV circuit uprate	18/02/2021	02/06/2022	03/11/2025
CP0823	Maynooth - Turlough Hill 220 kV line refurbishment	30/06/2017	05/12/2024	01/11/2026
CP0824	Moneypoint - Oldstreet 400 kV line refurbishment	17/09/2014	20/06/2018	30/06/2023
CP0825	Oldstreet Woodland 400 kV Line refurbishment	25/03/2013	19/03/2015	07/07/2023
CP0829	Clashavoon Macroom No1 110 kV circuit & associated station works & 250 MVA transformer	25/06/2014	16/01/2018	26/11/2021
CP0835	Coolnabacky - Portlaoise 110 kV line uprate	30/05/2018	06/12/2024	01/12/2025
CP0837	Bellacorrick 110 kV Station T141 Uprate	10/12/2014	07/12/2018	10/11/2023
CP0839	Moy 110 kV Station reconfiguration and busbar uprate	30/09/2014	07/10/2015	18/10/2024
CP0841	Arva - Carrick-on-Shannon 110 kV line uprate	21/05/2020	15/12/2021	30/11/2025
CP0848	Castlebar-Cloon 110 kV Line Uprate-Refurb	16/09/2020	20/12/2023	01/12/2025
CP0857	Paint Towers Nationwide	17/02/2014	24/11/2014	31/10/2026
CP0866	Great Island - Kellis 220 kV Line Uprate	16/11/2022	30/06/2025	30/11/2029
CP0867	Flagford - Louth 220 kV Line Refurbishment	20/04/2015	30/04/2020	30/11/2025
CP0868	Knockraha - Raffeen 220 kV line refurbishment	30/10/2015	25/09/2019	27/07/2021
CP0869	Maynooth - Woodland 220 kV line uprate	15/08/2019	17/12/2020	30/11/2024
CP0871	Galway 110 kV Station Redevelopment Project	21/06/2017	21/12/2018	30/11/2024
CP0872	West Dublin New 220-110 kV Station (Castlebagot 220 kV Station)	07/07/2014	17/05/2017	12/11/2024
CP0873	Dunstown - Moneypoint 400 kV Refurbishment	20/06/2014	05/12/2019	30/11/2026
CP0878	Binbane 110 kV Station - Gate 3 DSO Wind Generation	16/07/2014	25/05/2018	10/06/2022
CP0883	Ballyvouskill Knockanure 220 kV Line Uprate	24/02/2016	28/09/2018	19/09/2022
CP0894	Great Island 110-38 kV trafo DSO and bay works	10/03/2015	11/07/2016	02/07/2021
CP0901	Kilbarry - Knockraha 110 kV No 2 Line Refurbishment	13/05/2020	03/10/2022	10/11/2025
CP0902	Tarbert - Trien 110 kV No 1 Line Refurbishment	15/03/2016	27/09/2017	30/11/2022
CP0903	Cloon - Lanesboro 110 kV No 1 Line Refurbishment	15/06/2016	10/09/2020	05/10/2022
CP0905	Louth - Rathrussan 110 kV No 1 Line Uprate	25/05/2016	30/06/2022	30/09/2025
CP0907	Dalton 110 kV Busbar	01/10/2021	06/09/2023	24/11/2026
CP0913	Flagford Sligo 110 kV Line Conflict	05/02/2015	22/12/2015	31/10/2017
CP0917	Prospect Tarbert 220 kV Cable Replacement Project	16/06/2021	14/06/2024	28/11/2025
CP0919	Lanesboro 110 kV Station Redevelopment Project	28/12/2017	30/06/2020	30/11/2029
CP0933	Thurles 110 kV Station - Statcom	22/10/2015	19/10/2020	18/01/2024
CP0934	Ballynahulla 220-110 kV Station - Statcom	22/10/2015	04/07/2019	21/11/2023
CP0935	Ballyvouskill 220-110 kV Station - Statcom	22/10/2015	04/07/2019	12/10/2023
CP0936	Knockanure Reactor	15/08/2015	15/04/2019	01/11/2021
CP0945	Great Island Kilkenny 110 kV Uprate	31/03/2017	13/12/2019	30/06/2022
CP0949	Kilbarry 110 kV GIS Station	14/02/2017	04/03/2021	10/11/2025
CP0966	Kildare Meath***	24/03/2021	29/11/2024	22/09/2028
CP0967	Moneypoint 400 kV Series Capacitor	31/08/2015	13/12/2024	31/12/2027
CP0968	Dunstown 400 kV Series Capacitor	15/06/2016	13/12/2023	01/07/2027
CP0969	Oldstreet-Woodland 400 kV Series Capacitor	15/06/2016	13/12/2023	09/08/2027
CP0970	Cross Shannon 400 kV Cable	21/09/2016	16/12/2021	22/05/2026
CP0972	Wexford 110 kV Busbar Uprate	21/09/2016	14/05/2018	13/07/2021
CP0973	Knockraha Short Circuit Rating Mitigation	03/11/2016	21/06/2019	03/11/2025
CP0982	Flagford Sligo Capacity Needs	31/05/2024	03/11/2025	31/12/2027
CP0983	Point on Wave Controller for Glanagow 220 kV Station	04/08/2016	23/05/2017	10/11/2025
CP0984	Belcamp Shellybanks 220 kV Cable*	01/07/2016	15/07/2020	
CP1000	Lanesboro - Mullingar 110 kV Thermal Uprate	29/01/2021	10/09/2024	30/11/2025
CP1001	Corduff - Finglas 1 & 2 220 kV line refurbishment	10/11/2022	28/03/2024	30/10/2025
CP1002	Cushaling - Newbridge 110 kV Thermal Uprate	30/03/2023	19/12/2025	30/11/2029
CP1003	Cushaling - Portlaoise 110 kV line uprate	05/07/2023	05/12/2025	30/11/2029
CP1004	Killonan - Limerick No 1 110 kV line refurbishment	09/09/2024	30/09/2026	05/12/2029
CP1009	Cruiserath (Amazon) 220 kV Permanent Connection	29/09/2017	25/11/2020	29/06/2022
CP1011	Carrickalangan 110 kV station	26/07/2019	18/12/2020	29/07/2022
CP1014	Gemini (Snugborough) Phase 2	19/04/2018	22/02/2019	17/12/2021
CP1017	400 kV Voltage Uprate Trial	25/09/2017	28/04/2020	31/03/2022
CP1019	Cashla Tynagh 220 kV Line Fibre Wrap	08/09/2017	11/06/2018	30/04/2021
CP1020	Blundelstown 110 kV Station	26/01/2018	11/09/2020	31/08/2023
CP1021	East Meath - North Dublin Reinforcement***	07/06/2022	30/06/2025	14/12/2029
CP1022	Maynooth - Turlough Hill PLC Replacement	22/06/2018	06/12/2019	10/07/2025
CP1023	Letterkenny station redevelopment	17/06/2021	25/06/2025	28/09/2029
CP1025	Corduff 110 kV Station Development Project	03/05/2018	17/05/2019	27/05/2021
CP1029	Capital Project 1029	15/05/2019	31/10/2019	31/01/2023
CP1031	Flagford 220 kV Station Sprecher & Schuh CB Replacement	30/06/2018	11/07/2019	20/11/2026
CP1032	Cashla 220 kV Station Sprecher & Schuh CB Replacement	30/06/2018	11/07/2019	30/11/2026
CP1037	Kilbarry Line Conflicts	05/07/2018	20/11/2019	19/03/2021
CP1040	Rosspile 110 kV station	06/11/2018	15/07/2021	24/10/2022
CP1041	Timahoe 110 kV Station	06/11/2018	21/10/2021	26/07/2024
CP1047	Oweninny Power 2	05/11/2020	01/12/2021	01/12/2023

Project Code	Project Name	GW3 (CA)	GW6 (PA)	Energisation (EI)
CP1048	Power Flow Control Scheme	04/02/2021	22/04/2025	29/11/2027
CP1049	Bracetown 220 kV Station	14/06/2019	30/01/2020	30/06/2021
CP1051	Gallinstown Solar 110 kV Station	06/11/2018	19/11/2020	08/08/2022
CP1055	Harristown Solar Farm	20/12/2018	19/11/2020	31/10/2026
CP1058	Shannonbridge A - New 220 kV transformer bay	16/05/2019	12/06/2020	30/04/2021
CP1059	Shannonbridge B - Raghra station	28/05/2021	12/10/2022	30/06/2025
CP1060	Loughteague 110 kV solar farm	03/06/2020	05/11/2021	30/11/2026
CP1062	Drombeg Solar - 110 kV Station	28/06/2019	17/12/2020	13/05/2025
CP1064	Finglas Pantograph Replacement Project	20/12/2019	12/11/2020	31/10/2025
CP1065	ESB GWM - T104 Ardnacrusa	06/12/2018	11/04/2019	12/08/2021
CP1068	Tullabeg Solar 110 kV Station	05/09/2019	01/04/2021	20/12/2023
CP1069	Ballinknockane Solar Farm*	16/05/2019	24/12/2020	30/04/2026
CP1073	Croaghau West 110 kV Station	02/07/2020	24/01/2025	03/04/2028
CP1075	Kelwin Power Plant Phase 2	09/09/2019	22/09/2020	30/11/2020
CP1077	Temporary 50 Mvar reactor in Ballyvouskil	01/08/2019	18/11/2020	22/10/2021
CP1078	Lanesboro - Sliabh Bawn 110 kV Line Uprate	18/02/2021	06/03/2024	30/11/2025
CP1079	Binbane - Cathaleen - s Fall 110 kV Line uprate	29/01/2021	07/06/2023	11/09/2024
CP1083	Gorman Energy Storage	07/11/2019	17/12/2020	18/12/2021
CP1084	Lisdrumdoagh 110 kV Battery Storage	06/02/2020	26/05/2021	19/12/2021
CP1085	Aghada Battery Storage	05/12/2019	22/03/2021	03/12/2021
CP1086	Dunstown T4201 and Woodland T4201 Transformer replacement	01/05/2023	31/07/2024	30/10/2028
CP1087	Porterstown Battery Storage	02/07/2020	22/03/2021	04/02/2022
CP1088	Greenlink Interconnector	20/02/2020	22/06/2022	28/06/2024
CP1089	Profile Park 110 kV Station	03/06/2020	31/08/2021	11/10/2022
CP1090	Rathmullan 110 kV Station	27/11/2020	18/06/2021	04/11/2023
CP1091	New 400 220 kV Transformer for Moneypoint Sub-Station	18/12/2019	02/10/2020	10/11/2023
CP1092	New 400 kV Strategic Spare Transformer	29/01/2020	15/12/2022	27/06/2025
CP1093	Barnageeragh 110 kV Station	09/03/2020	22/12/2020	01/11/2024
CP1094	Buffy 110 kV Station	10/02/2020	19/11/2020	05/05/2023
CP1096	Transformer protection upgrade, 6 Stations	10/02/2020	02/10/2020	30/11/2025
CP1099	Lisheen 3 Windfarm	25/06/2020	31/07/2021	18/11/2022
CP1100	Finglas - North Wall Cable Replacement***	28/06/2022	19/12/2024	02/07/2029
CP1101	Mullagharlin 110 kV Station - 2 New DSO Transformer Bays	04/03/2020	06/08/2020	17/12/2021
CP1102	Grangecastle South	13/05/2020	08/10/2021	12/05/2023
CP1103	Corduff FlexGen	02/04/2020	26/07/2022	07/02/2024
CP1104	Pollaphuca Refurbishment Project	08/09/2023	14/04/2025	31/05/2028
CP1105	Poolbeg BESS	16/04/2020	22/04/2022	12/06/2023
CP1106	Poolbeg FlexGen	16/04/2020	20/01/2022	06/11/2023
CP1109	Gorman and Connected Stations 220-110 kV Protection Upgrade	13/05/2020	25/06/2021	01/12/2025
CP1111	Ballydine, Cahir and Connected Stations 110 kV Protection Upgrade	21/05/2020	18/07/2021	30/11/2025
CP1112	Limerick and Connected Stations 110 kV Protection Upgrade	21/05/2020	19/12/2023	31/12/2025
CP1113	Corduff 220 kV Station Deep Works	17/08/2020	02/06/2021	20/03/2025
CP1114	Platin and Connected Stations 110 kV Protection Upgrade	13/05/2020	18/08/2021	30/11/2025
CP1115	Drybridge and Connected Stations 110 kV Protection Upgrade	13/05/2020	16/04/2021	30/11/2025
CP1116	Tipperary, Cahir and Connected Stations 110 kV Protection Upgrade	13/05/2020	14/07/2021	30/11/2025
CP1117	Irishtown FlexGen-BESS	25/06/2020	22/04/2022	20/12/2023
CP1119	Cashla Flagford 220 kV Line Refurbishment	26/02/2021	21/11/2024	18/12/2025
CP1120	Clonreen 110 kV Station	06/08/2020	20/05/2021	01/08/2022
CP1121	Arklow-Great Island-Lodge Wood 220kV Line Refurbishment	30/09/2024	30/09/2025	30/09/2028
CP1122	Physical Security of Transmission Stations - Dublin Region**	01/09/2020	08/12/2023	
CP1123	Physical Security of Transmission Stations - South Region**	07/05/2021	08/12/2023	
CP1124	Physical Security of Transmission Stations - North Region**	11/06/2021	08/12/2023	
CP1125	Physical Security of Transmission Stations - Central Region**	14/07/2021	08/12/2023	
CP1126	Mully Graffy Windfarm	06/08/2020	30/04/2025	31/10/2026
CP1127	Lenalea Windfarm	01/10/2020	05/10/2021	04/08/2023
CP1128	Ballyvatta solar farm - Knockraha	04/11/2021	01/04/2025	01/10/2026
CP1129	Aghada BESS 02	05/11/2020	17/12/2021	02/02/2024
CP1130	Cloghan Wind Farm- New 110 kV transformer Bay	06/08/2020	05/08/2021	07/11/2022
CP1131	Gillinstown Solar (Garballagh 110 kV Station)	05/11/2020	17/12/2021	10/02/2023
CP1132	Cow Cross New 110 kV Transformer	02/09/2020	07/10/2021	26/06/2024
CP1135	Golagh Windfarm Modification	05/11/2020	03/09/2021	01/04/2022
CP1136	Deenes 110 kV Station	19/11/2020	14/12/2022	18/09/2024
CP1137	Carlow, Kellis 110 kV Protection Upgrade	01/10/2020	01/09/2021	10/06/2025
CP1139	Sligo & Srananagh 220 & 110 kV Protection upgrade	01/10/2020	16/07/2021	30/11/2025
CP1140	Athy, Carlow and Connected Stations 110 kV Protection Upgrade	01/10/2020	16/07/2021	10/11/2025
CP1141	Kellis Station 220 kV & 110 kV Protection Upgrade	01/10/2020	01/09/2021	10/11/2025
CP1142	Firlough 110 kV Station (Firlough WF)	04/02/2021	30/04/2026	30/06/2027
CP1143	Derrylahan 110 kV Station (Blackwater Bog Solar)	12/06/2024	11/06/2025	17/02/2027
CP1144	Kinnegad 110 kV station, Derrylahan 110 kV bay conductor uprate	22/01/2021	01/12/2021	29/11/2025
CP1145	Rathnaskilloge Solar Farm	07/01/2021	25/12/2022	15/10/2024
CP1146	Carrickmines - Poolbeg 220 kV Cable Replacement***	16/12/2021	29/05/2026	20/06/2029
CP1149	Newbridge - Cushaling 110 kV line, Stations bay conductors and lead-in conductor uprate	22/01/2021	04/11/2021	10/11/2025
CP1150	Inchicore - Poolbeg 2 220 kV Cable Replacement***	16/12/2021	18/12/2025	28/09/2029
CP1152	Arva and Connected Stations 110 kV Protection Upgrade	12/11/2020	01/09/2021	12/12/2025
CP1153	Oldstreet Tynagh & Cashla 400 kV and 220 kV Protection Upgrade	12/11/2020	05/08/2021	28/11/2025
CP1154	Belcamp Land Acquisition**	19/11/2020	20/05/2024	
CP1155	Glenree - Moy 110 kV Line Uprate	15/04/2021	20/12/2023	30/06/2025
CP1156	Sligo 110 kV Station - Shrananagh 1 & 2 Bay uprates	18/06/2021	04/04/2022	30/11/2025
CP1157	Inchicore - Poolbeg 1 220 kV Cable Replacement***	20/12/2021	18/12/2025	02/08/2029
CP1158	Clonfad Solar	19/01/2021	22/12/2022	31/10/2025
CP1159	Cullenagh and connected stations protection upgrade	04/12/2020	04/11/2021	30/11/2025
CP1160	Coolroe, Inniscarra & connected stations protection upgrade	04/12/2020	04/11/2021	30/11/2024
CP1161	Cathaleens Fall and connected stations 110 kV protection upgrade	04/12/2020	01/12/2021	30/11/2025
CP1162	Irishtown, Shellybanks and connected stations 220 kV protection upgrade	04/02/2021	04/11/2021	30/11/2026
CP1163	Butlerstown, Killoteran & Waterford 110 kV protection upgrade	04/02/2021	04/11/2021	10/11/2025
CP1164	West Cork 110 kV protection upgrade	04/02/2021	03/02/2022	28/11/2025
CP1166	Gorman - Platin 110 kV line uprate	18/03/2021	18/07/2024	24/11/2025
CP1167	Drybride - Oldbridge - Platin 110 kV line uprate	18/03/2021	27/10/2023	25/11/2025
CP1168	Cashla-Salthill 110 kV Thermal Uprate	18/03/2021	02/08/2024	30/11/2025
CP1172	Crane - Wexford 110 kV Line uprate	17/06/2021	09/10/2023	30/11/2025
CP1173	Glencloosagh Phase 1 - Rotating Stabiliser	06/05/2021	30/06/2024	30/07/2025
CP1174	Aghaleague 110 kV Station	02/03/2022	17/03/2025	30/10/2025
CP1175	Kishoge 110 kV Station	09/08/2021	19/03/2024	22/11/2024
CP1176	Huntstown T2002 Customer Transformer connection	26/05/2021	31/07/2021	29/10/2021
CP1177	Whitegate 110 kV Station Refurbishment Project	30/07/2024	01/09/2025	01/12/2028

Project Code	Project Name	GW3 (CA)	GW6 (PA)	Energisation (EI)
CP1179	Cloghran Phase 2 Transformer Replacement	26/05/2021	12/08/2021	29/04/2022
CP1180	Moneypoint Synchronous Condenser	05/07/2021	10/02/2022	06/09/2022
CP1181	Corduff Platin 110 kV Line Conflict	30/08/2021	06/05/2022	30/10/2023
CP1182	Transformer Restoration Project	31/03/2023	25/07/2024	30/11/2029
CP1183	Mooretown 220 kV Station	06/04/2022	14/06/2024	01/12/2025
CP1186	Agannnygal, Ennis and connected stations 110 kV Protection Upgrade	05/08/2021	08/09/2022	31/12/2025
CP1188	Kilcarbery*	08/07/2021	30/06/2024	27/06/2025
CP1190	Poolbeg 220 kV Station***	16/12/2021	17/12/2024	20/07/2027
CP1191	Cashla-Galway 110 kV cct 1 Line uprate	21/11/2022	29/12/2025	30/11/2029
CP1194	Woodland 400 kV Station Redevelopment	21/03/2022	14/12/2023	30/11/2028
CP1195	Turlough Hill 220 kV Station Refurbishment	06/09/2023	01/07/2026	03/12/2029
CP1196	Arklow - Ballybeg - Carrickmines 110 kV capacity Needs	28/06/2024	01/03/2026	01/12/2030
CP1197	Dunstown Asset Replacements	31/12/2021	19/12/2023	03/12/2029
CP1198	Barnakyle MIC Increase	27/10/2022	30/06/2025	30/06/2026
CP1199	Derryiron - Thornsberry 110 kV Line Uprate	19/11/2021	20/12/2023	25/10/2027
CP1200	Carrickmines Area 220 kV Cable Ducting	30/09/2021	20/12/2022	31/03/2025
CP1201	Bogtown 110 kV Station	07/10/2021	10/11/2022	15/05/2024
CP1207	Lisheen - Thurles 110 kV Protection Upgrade	04/11/2021	25/10/2022	30/07/2025
CP1209	Brown Boveri Circuit Breaker Replacements	31/03/2022	20/12/2023	01/12/2028
CP1211	Bandon Dunmanway 110 kV circuit thermal capacity	21/01/2022	30/09/2024	27/11/2026
CP1212	Bandon Raffeen 110 kV circuit thermal capacity	28/01/2022	31/12/2024	31/12/2027
CP1213	Belcamp 220 kV Busbar Extension***	15/12/2021	27/09/2024	23/12/2027
CP1214	North County Dublin Bulk Supply Point and Associated New Transmission Circuit* ***	18/10/2024		
CP1215	Knockraha station Celtic IC Non contested works	23/02/2022	06/12/2023	31/12/2026
CP1216	Poolbeg - North Wall 220 kV Cable Replacement***	31/05/2022	18/08/2025	01/12/2028
CP1217	Philipstown 110 kV Station	03/02/2022	25/10/2023	30/06/2025
CP1219	Coole Wind Farm	01/02/2022	30/03/2025	29/08/2025
CP1220	Garrintaggart 110 kV Station - Pinewoods Wind Farm	01/02/2022	12/01/2024	29/08/2025
CP1221	Mulgeeth 110 kV Station - Drehid Wind Farm	01/02/2022	30/03/2025	25/09/2026
CP1222	Knockraha 220 kV Transformer Replacement	19/01/2022	15/12/2022	10/10/2025
CP1223	Bandon 110 kV Busbar Rating Needs	03/05/2023	30/06/2025	03/12/2029
CP1224	Lysaghtstown 110 kV Station	03/02/2022	02/03/2023	21/12/2023
CP1225	Finglas - Corduff 220 kV Protection Upgrade	03/02/2022	13/12/2022	30/11/2026
CP1226	South Dublin Reinforcement combined with West County Dublin Bulk Supply Point (BSP)* ***	01/11/2024		
CP1227	Cashla and Connected Stations 220 kV & 110 kV Protection Upgrade	02/02/2022	21/09/2022	30/11/2026
CP1228	Shannonbridge and Connected Stations 220 kV & 110 kV Protection Upgrade	03/02/2022	26/09/2022	30/11/2026
CP1229	Lislea 110 kV Station - Drumlins WF	29/04/2022	22/12/2022	09/12/2023
CP1230	Darndale Phase 2 - 3 110 kV customer connections in Darndale 110 kV station	17/06/2022	19/12/2022	19/08/2024
CP1231	Knockdrin 110 kV Station (Yellow River Wind Farm)	07/04/2022	05/09/2023	15/09/2025
CP1232	Derryiron 110 kV Busbar Uprate	29/04/2022	05/07/2023	31/12/2025
CP1233	Donegal - Srananagh Corridor**	29/11/2024		
CP1234	Laurencetown 110 kV Station (Clonin North Solar Farm)	07/04/2022	16/10/2023	14/11/2025
CP1235	Louth - Woodland 220 kV Uprate	28/04/2022	02/06/2025	03/12/2029
CP1236	Timoney 110 kV Station*	07/07/2022	23/04/2024	31/03/2025
CP1237	Ferry View 110 kV Station*	07/07/2022	01/10/2025	01/10/2026
CP1238	Arklow 220 kV Station Redevelopment*	20/04/2023	01/09/2025	01/09/2029
CP1240	Coumadovane Solar Extension*	31/08/2022	30/09/2025	30/10/2026
CP1241	Belcamp BSP Transfer	01/09/2022	01/05/2024	01/04/2025
CP1242	Great Island 220-110 kV transformer upgrades	07/12/2022	20/12/2023	01/11/2028
CP1244	North Arklow Solar Plus Storage	06/10/2022	26/02/2024	30/09/2025
CP1245	Castletreasure 110 kV Station (Ballinrea Solar Park)	09/09/2022	09/09/2024	28/11/2025
CP1246	Coomnaclohy 110 kV Station*	07/07/2022	30/08/2024	30/06/2025
CP1247	New Ballyvouskill 220-110 kV Transformer	10/05/2022	28/08/2023	29/12/2026
CP1248	Harlockstown Solar (Gallanstown Ext)	01/06/2022	20/12/2023	08/03/2024
CP1249	Porterstown Battery Phase2	01/06/2022	30/11/2023	24/03/2025
CP1250	Sprecher and Schuh Circuit Breaker replacement	09/10/2023	12/06/2025	14/03/2030
CP1251	North Wall Station refurbishment* ***	30/07/2024		
CP1255	Castlelost FlexGen	04/05/2022	28/08/2023	10/04/2025
CP1256	Greener Ideas Profile Park	05/05/2022	15/04/2024	02/07/2025
CP1257	Kilshane Power Station	05/05/2022	29/07/2024	01/12/2025
CP1259	Cuilleen Power	05/05/2022	20/03/2024	23/11/2025
CP1260	Dennistown 110kV Substation*	30/05/2022	30/06/2024	30/06/2025
CP1262	Shanonagh 110kV Station	10/11/2022	26/07/2024	31/10/2026
CP1264	Rhode ESS	23/06/2022	01/09/2023	26/06/2026
CP1265	Corkagh 110kV Station Phase 2	26/07/2022	25/10/2023	24/07/2025
CP1267	Arklow 220kV - DSO Ballymanus WF	30/09/2022	06/11/2023	01/12/2025
CP1268	Dunfirth 110kV - DSO Dysart PV	30/09/2022	18/04/2024	01/08/2025
CP1269	The Dell Solar Lodgewood 220kV Crory Station	01/09/2022	20/12/2023	16/04/2026
CP1272	Derryiron Temporary By Pass Project	12/10/2022	28/07/2023	16/04/2024
CP1273	Dublin Central Bulk Supply Point* ***	19/06/2024		
CP1274	CP1274 Temporary 220kV Cable Diversion of Castlelost Site - Major Conflict	06/09/2022	12/06/2023	22/12/2023
CP1275	Cashla-Galway 110 kV cct 2 Uprating	21/11/2022	30/12/2025	31/12/2029
CP1276	Cashla-Galway 110 kV cct 3 Uprating	21/11/2022	30/12/2025	31/12/2029
CP1277	Intel 110kV line diversion	30/11/2022	06/11/2024	11/05/2026
CP1280	Ballyragget Future Proofed Cable	25/01/2024	16/12/2024	01/04/2026
CP1281	Batter Lane DSO Station	09/02/2023	01/05/2024	01/04/2025
CP1282	Clogher-Drumkeen 110 kV Line Alteration*	31/03/2023	01/04/2025	31/12/2026
CP1284	Walterstown 110kV Station DSO	15/12/2023	10/10/2025	10/10/2027
CP1285	Barnahely-Raffeen No2 110 kV Line	30/04/2024	31/03/2025	21/02/2028
CP1286	Tonroe 110kV Station DSO	11/08/2023	30/04/2024	23/09/2025
CP1287	Ringsend Cable Diversion	15/10/2023	09/09/2024	13/11/2025
CP1291	Carlow 110 kV Station Busbar Thermal Capacity Need	07/06/2023	20/12/2024	22/11/2029
CP1296	Rinawade 110 kV GIS Station (Liffey Park)	06/11/2023	08/07/2024	31/03/2027
CP1297	Glansillagh 220kV Station S	08/06/2023	22/05/2025	01/11/2028
CP1300	Climate Change Adaptation Measures**	05/04/2023	30/09/2025	
CP1301	Dundalk Louth 110 kV Line Uprate*	07/02/2024	30/12/2025	30/11/2028
CP1302	Killonan Shannonbridge 220 kV Line Refurbishment	10/06/2025	01/06/2027	01/06/2030
CP1304	Strategic Spares for OHL, Stations and Cables**	08/03/2023	20/09/2024	
CP1310	Agannnygal-Ennis Line Refurbishment	09/12/2024	30/09/2026	30/11/2029
CP1311	Athlone - Lanesboro 110 kV line uprate	16/02/2023	30/09/2025	30/11/2029
CP1312	Athy - Carlow 110 kV circuit 1	08/12/2025	15/11/2027	01/01/2030
CP1314	Baroda - Monread 110 kV circuit 1	02/12/2024	01/03/2027	01/10/2030
CP1315	Baroda - Newbridge 110 kV circuit 1 (DLR)	01/03/2026	01/03/2028	01/10/2030
CP1316	Battery Upgrades-Diesel Generator upgrades	29/03/2024	30/06/2025	30/12/2026
CP1318	Binbane - Clogher - Cathaleens Fall - 110 kV Clogher tie in	02/12/2024	01/12/2027	17/12/2029

Project Code	Project Name	GW3 (CA)	GW6 (PA)	Energisation (EI)
CP1319	Blake Maynooth Newbridge refurbishment	13/06/2025	30/09/2026	30/11/2029
CP1320	Barrymore Cahir Knockraha 110kV Line Uprate	31/07/2022	06/03/2025	01/11/2028
CP1321	Cashla - Dalton 110 kV circuit 1 (DLR)	23/03/2023	20/12/2024	28/11/2025
CP1322	Cathaleens Fall - Coraclasy 110 kV circuit 1 (DLR)	05/04/2023	30/12/2024	28/11/2025
CP1324	Clashavoon - Knockraha or Cullenagh - Knockraha 220 kV lines (PFC)	10/09/2025	08/09/2026	31/10/2028
CP1325	Corduff Mullingar Partial Line uprate	30/09/2024	30/06/2026	30/11/2029
CP1327	Drumkeen - Clogher 110 kV circuit 1	05/12/2024	19/07/2026	10/09/2028
CP1329	Stonestown 110 kV Station	11/01/2023	02/10/2023	19/08/2024
CP1331	ECP 2-3-11 - Connections Project Placeholder	31/05/2024	30/05/2025	26/07/2027
CP1332	ECP 2-3-12 - Connections Project Placeholder	27/09/2024	30/09/2025	28/06/2028
CP1333	ECP 2-3-13 - Connections Project Placeholder	01/07/2024	15/02/2025	16/11/2027
CP1334	Newbarn 110 kV Station	01/08/2023	29/11/2024	01/06/2027
CP1335	Garballagh 110kV Station	20/07/2023	29/09/2024	20/02/2025
CP1338	Effernoge 110kV Station	01/11/2023	28/05/2025	15/07/2027
CP1341	Cloon 110 kV	04/04/2023	13/09/2024	28/04/2027
CP1342	Drumcamill 110 kV Station*	26/09/2023	09/09/2024	08/06/2027
CP1344	ECP 2-3-23 - Connections Project Placeholder	30/06/2024	28/01/2025	28/10/2027
CP1345	Golagh 110kV Station	16/02/2024	27/05/2025	25/11/2027
CP1346	Meath Hill 110 kV Station	27/03/2024	30/03/2025	31/08/2027
CP1347	Dunbrody 110 kV Station	14/06/2023	01/04/2025	08/06/2027
CP1351	Ballynadridden 110 kV Station	06/01/2023	30/04/2024	22/10/2026
CP1352	Gortatleva 110 kV Station	09/04/2023	29/07/2024	28/04/2027
CP1353	Bendinstown 110kV Station	20/04/2023	15/07/2024	20/04/2027
CP1354	Coolshamroge 110 kV Station	05/04/2023	31/03/2025	29/09/2025
CP1355	Corbetstown 110 kV Station	23/08/2023	31/03/2025	31/12/2027
	ECP 2-3-10 - Connections Project Placeholder	15/05/2024	31/03/2025	31/12/2027
	ECP 2-3-11 - Connections Project Placeholder	15/05/2024	31/03/2025	31/12/2028
	ECP 2-3-12 - Connections Project Placeholder	15/05/2024	31/03/2025	31/12/2028
	ECP 2-3-13 - Connections Project Placeholder	28/06/2024	30/06/2025	31/03/2029
	ECP 2-3-14 - Connections Project Placeholder	28/06/2024	30/06/2025	31/03/2027
	ECP 2-3-15 - Connections Project Placeholder	28/06/2024	30/06/2025	31/03/2028
	ECP 2-3-16 - Connections Project Placeholder	28/06/2024	30/06/2025	31/03/2028
	ECP 2-3-17 - Connections Project Placeholder	28/06/2024	30/06/2025	31/03/2028
	ECP 2-3-18 - Connections Project Placeholder	28/06/2024	30/06/2025	31/03/2028
	ECP 2-3-19 - Connections Project Placeholder	28/06/2024	30/06/2025	31/03/2028
	ECP 2-3-02 - Connections Project Placeholder	30/06/2024	31/03/2025	31/12/2027
	ECP 2-3-20 - Connections Project Placeholder	28/06/2024	30/06/2025	31/03/2028
	ECP 2-3-21 - Connections Project Placeholder	28/06/2024	30/06/2025	31/03/2028
	ECP 2-3-22 - Connections Project Placeholder	28/06/2024	30/06/2025	31/03/2029
	ECP 2-3-23 - Connections Project Placeholder	28/06/2024	30/06/2025	31/03/2028
	ECP 2-3-24 - Connections Project Placeholder	28/06/2024	30/06/2025	31/03/2028
	ECP 2-3-25 - Connections Project Placeholder	30/09/2024	30/09/2025	30/06/2028
	ECP 2-3-26 - Connections Project Placeholder	30/09/2024	30/09/2025	30/06/2027
	ECP 2-3-03 - Connections Project Placeholder	15/05/2024	31/03/2025	31/12/2027
	ECP 2-3-04 - Connections Project Placeholder	15/05/2024	31/03/2025	31/12/2027
	ECP 2-3-05 - Connections Project Placeholder	15/05/2024	31/03/2025	31/12/2027
	ECP 2-3-06 - Connections Project Placeholder	15/05/2024	31/03/2025	31/12/2027
	ECP 2-3-07 - Connections Project Placeholder	15/05/2024	31/03/2025	31/12/2027
	ECP 2-3-08 - Connections Project Placeholder	15/05/2024	31/03/2025	31/12/2027
	ECP 2-3-09 - Connections Project Placeholder	15/05/2024	31/03/2025	31/12/2027
CP1381	Flagford - Sliabh Bawn - Lanesboro 110 kV lines (PFC)	12/12/2025	19/11/2027	01/01/2030
CP1383	Killonan - Knockraha 220 kV line (PFC)	10/09/2025	17/11/2027	01/01/2030
CP1384	Kilteel - Maynooth 110 kV line uprate	30/11/2024	01/03/2027	01/11/2030
CP1387	Letterkenny - Cathaleen_s or Letterkenny - Clogher 110 kV lines (PFC)	10/09/2025	06/02/2026	31/03/2028
CP1388	Letterkenny - Tievebrack - Binbane 110 kV lines (PFC)	10/09/2025	19/07/2026	10/09/2028
CP1389	Limerick - Rathkeale Line Refurbishment	12/08/2024	01/05/2026	03/12/2029
CP1390	Maynooth - Rinawade 110V line uprate	06/06/2023	07/03/2025	01/11/2029
CP1391	Maynooth-Derryiron-Timahoe 110 kV Line Uprate	05/04/2023	30/09/2025	08/11/2029
CP1393	Offshore Phase 1 Project 1*	15/12/2022	31/12/2024	30/06/2027
CP1394	Offshore Phase 1 Project 2*	15/12/2022	31/12/2024	30/06/2027
CP1396	Offshore Phase 1 Project 4*	15/12/2022	31/12/2024	30/06/2027
CP1397	Offshore Phase 1 Project 5*	15/12/2022	31/12/2024	30/06/2027
CP1398	Offshore Phase 1 Project 7*	15/12/2022	31/12/2024	30/06/2027
CP1402	Platin 110kV Station Refurbishment	01/09/2024	01/09/2025	01/09/2029
CP1403	Rinawade - Dunfirth 110 kV uprate	18/05/2023	02/06/2026	28/09/2029
CP1404	Sligo - Srananagh - Corderry 110 kV lines (PFC)	11/12/2025	18/11/2027	01/01/2030
CP1412	Knockraha 220 kV Transformer Replacement (T2102)	08/03/2023	05/09/2024	05/11/2027
CP1414	Kilcumber 110 kV Station	06/09/2023	15/05/2024	03/10/2024
CP1422	Cashla - Prospect 220kV	12/03/2025	03/09/2026	30/11/2029
CP1423	Cashla - Tynagh 220kV	14/04/2025	16/09/2026	30/11/2029
CP1428	Cashla Dalton 110kV Thermal Capacity Increase	12/12/2023	30/03/2025	30/09/2029
CP1429	Castlebar Dalton 110kV Thermal Capacity Increase	12/12/2023	30/03/2025	30/09/2028
CP1435	Drumline Ennis 110kV circuit DLR and related works	04/03/2024	31/03/2025	30/09/2028
CP1436	Ardnacrusha Ennis 110kV circuit DLR and related works	04/03/2024	31/03/2025	20/12/2027
CP1437	Clahane-Tralee 110 kV Circuit Alteration CAR	27/09/2023	30/07/2024	11/10/2024
CP1438	Glanagow - Raffeen 220kV Circuit Alteration - Major Conflict*	14/09/2023	18/05/2024	
CP1442	Fosterstown 110 kV Station Connection DSO	20/02/2024	22/12/2025	27/11/2028
CP1449	Midleton 110kV Transformer Uprate and Station works DSO	20/02/2024	20/02/2025	19/12/2025
CP1450	Ardnacrusha Drumline 110kV thermal capacity needs	04/03/2024	30/06/2025	30/06/2028
CP1456	Clutterland 110kV Station Phase 2	20/02/2024	20/12/2024	20/02/2026
CP1460	Balruntagh 110kV Station	30/05/2024	25/02/2025	30/03/2028
CP1464	Tullabeg Phase 2	01/07/2024	31/03/2025	30/03/2028
CP1467	Caherhurlly 110 kV Station	30/05/2024	26/06/2025	23/12/2027
CP1468	Kilvinoge 110 kV Station	30/05/2024	26/06/2025	27/12/2027
