ID	% Complete	Node	Projects	Task Name	Duration	Start	Finish
1	**74%**			**Gate 3 Programme**	**741 days**	**Tue 15/07/08**	**Mon 18/07/11**
2	**85%**			**CER**	**538 days**	**Thu 13/11/08**	**Mon 31/01/11**
3	100%			CER Proposed Direction	0 days	Thu 13/11/08	Thu 13/11/08
4	100%			CER Final Direction	0 days	Tue 16/12/08	Tue 16/12/08
5	100%			CER confirm what conventional units and non GPA to add to ITC model and how to include them. Also what	0 days	Fri 16/01/09	Fri 16/01/09
6	100%			Confirmation of final list of applications and MECs	11 days	Fri 19/12/08	Fri 16/01/09
7	100%			Confirm transmission standard costs and lead times	64 days	Fri 30/01/09	Fri 01/05/09
8	100%			Proposed Treatment of Conventional Applications	81 days	Wed 01/04/09	Fri 24/07/09
9	100%			Final Direction on treatement of Conventional Applications	103 days	Mon 27/07/09	Fri 18/12/09
10	100%			Treatment of Renewable, Small and Low Carbon Generators outside the GPA	132 days	Mon 19/01/09	Fri 24/07/09
11	100%			Connection Policy	147 days	Mon 05/01/09	Fri 31/07/09
12	**81%**			**All-Island dispatch and scheduling**	**511 days**	**Mon 05/01/09**	**Mon 31/01/11**
13	100%			Initial Consultation Paper	130 days	Mon 05/01/09	Wed 08/07/09
14	100%			Proposed Position Paper	284 days	Thu 09/07/09	Thu 02/09/10
15	0%			Final Position Paper	97 days	Fri 03/09/10	Mon 31/01/11
16	**100%**			**Joint Pricing Principles and Losses Paper**	**258 days**	**Mon 01/06/09**	**Thu 17/06/10**
17	100%			Decision Paper on Joint Pricing Principles	258 days	Mon 01/06/09	Thu 17/06/10
18	100%			Losses policy for distribution connected generators	163 days	Mon 01/06/09	Fri 29/01/10
19	**100%**			**Contracts Process**	**261 days**	**Mon 31/08/09**	**Tue 21/09/10**
20	100%			DSO Standard Connection Agreement	78 days	Mon 31/08/09	Thu 17/12/09
21	100%			Decision on the process for fixed contracts approach	261 days	Mon 31/08/09	Tue 21/09/10
22	0%			**Decision on TLAFs methodology**	206 days	Fri 27/11/09	Fri 01/10/10
23	**100%**			**Review Firm Access Results**	**89 days**	**Fri 11/09/09**	**Thu 28/01/10**
24	100%			2010-2013	10 days	Fri 11/09/09	Thu 24/09/09
25	100%			2014-2017	10 days	Fri 04/12/09	Thu 17/12/09
26	100%			2018-2021	4 days	Fri 15/01/10	Wed 20/01/10
27	100%			2022-2025	4 days	Mon 25/01/10	Thu 28/01/10
28	**71%**			**DSO**	**614 days**	**Wed 21/01/09**	**Fri 15/07/11**
29	**100%**			**Produce Shallow Connections**	**408 days**	**Wed 21/01/09**	**Fri 10/09/10**
30	100%			Area K	135 days	Wed 21/01/09	Fri 31/07/09
31	100%			Area D	178 days	Wed 21/01/09	Thu 01/10/09
32	100%			Area H2	152 days	Tue 05/05/09	Fri 04/12/09
33	100%			Area H1	187 days	Mon 02/03/09	Tue 24/11/09
34	100%			Area B	195 days	Mon 09/02/09	Fri 13/11/09
35	100%			Area E	283 days	Wed 21/01/09	Fri 12/03/10
36	100%			Area J	156 days	Tue 01/09/09	Fri 23/04/10
37	100%			Area F	204 days	Mon 08/06/09	Wed 07/04/10
38	100%			Area A	235 days	Tue 04/08/09	Mon 19/07/10
39	100%			Area G	153 days	Tue 05/01/10	Thu 12/08/10
40	100%			Area C	127 days	Mon 01/02/10	Tue 03/08/10
41	100%			Area I	135 days	Mon 01/03/10	Fri 10/09/10
42	100%			Initial Connection Leadtimes for Constraints Analysis	0 days	Fri 31/07/09	Fri 31/07/09
43	**100%**			**DSO Cluster Customer Connection Method Meetings**	**287 days**	**Fri 01/05/09**	**Wed 30/06/10**
44	100%			Area K	12 days	Fri 01/05/09	Tue 19/05/09
45	100%			Area D	13 days	Mon 06/07/09	Wed 22/07/09
46	100%			Area H2	18 days	Mon 31/08/09	Wed 23/09/09
47	100%			Area H1	34 days	Mon 20/07/09	Fri 04/09/09
48	100%			Area B	29 days	Mon 13/07/09	Fri 21/08/09
49	100%			Area E	118 days	Mon 06/07/09	Fri 18/12/09
50	100%			Area J	79 days	Mon 12/10/09	Fri 12/02/10
51	100%			Area F	38 days	Mon 23/11/09	Wed 27/01/10
52	100%			Area A	133 days	Fri 16/10/09	Mon 10/05/10
53	100%			Area G	52 days	Mon 22/03/10	Thu 03/06/10
54	100%			Area C	44 days	Mon 15/03/10	Tue 18/05/10
55	100%			Area I	42 days	Fri 30/04/10	Wed 30/06/10
56	**64%**			**Application Fees**	**289 days**	**Tue 27/10/09**	**Fri 07/01/11**
57	100%			Invoice fees for offers due to issue in 2009	4 days	Tue 27/10/09	Fri 30/10/09
58	100%			Invoice fees for offers due to issue in 2010	5 days	Mon 04/01/10	Fri 08/01/10
59	0%			Invoice fees for offers due to issue in 2011	5 days	Mon 03/01/11	Fri 07/01/11
60	**15%**			**Issue Offers [CER-08-260]**	**367 days**	**Mon 14/12/09**	**Mon 20/06/11**
61	100%			Area K	10 days	Mon 14/12/09	Fri 08/01/10
62	100%			Area D	10 days	Mon 22/03/10	Fri 02/04/10
63	80%			Area H2	11 days	Thu 15/07/10	Thu 29/07/10
64	0%			Area H1	16 days	Fri 27/08/10	Fri 17/09/10
65	0%			Area B	15 days	Wed 22/09/10	Wed 13/10/10
66	0%			Area F	20 days	Wed 27/10/10	Tue 23/11/10
67	0%			Area E	20 days	Tue 08/02/11	Mon 07/03/11
68	0%			Area J	15 days	Wed 23/03/11	Wed 13/04/11
69	0%			Area A	15 days	Fri 20/05/11	Fri 10/06/11
70	0%			Area G	25 days	Thu 12/05/11	Thu 16/06/11
71	0%			Area C	15 days	Tue 24/05/11	Tue 14/06/11
72	0%			Area I	14 days	Tue 31/05/11	Mon 20/06/11
73	**11%**			**Issue Offers [CER 10/056]**	**236 days**	**Fri 30/07/10**	**Fri 15/07/11**

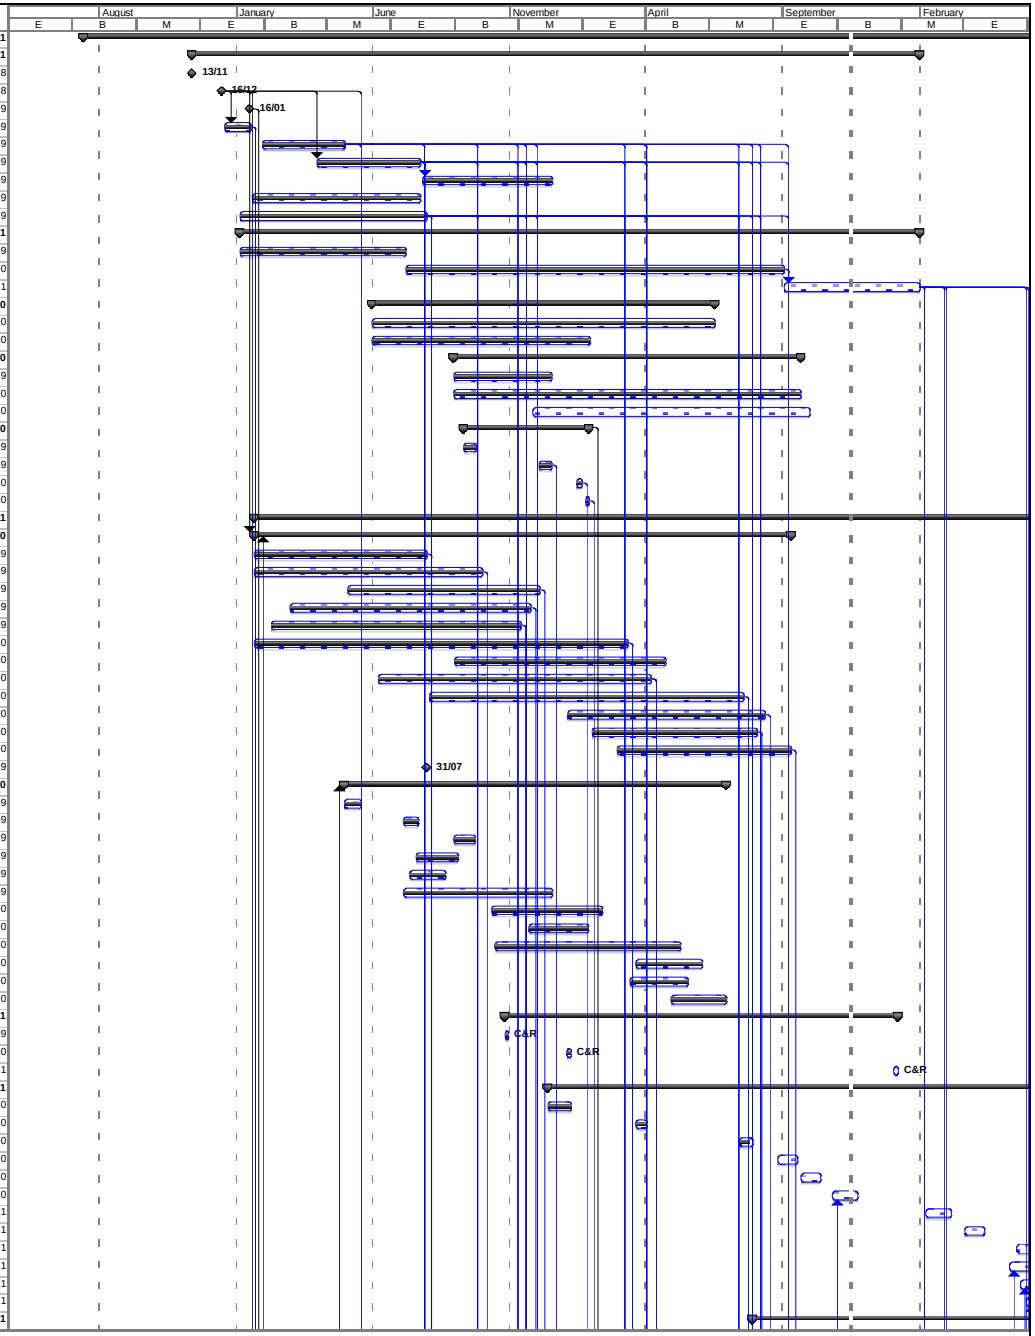

Project: Gate 3 Connection Offer Proces
Date: Mon 15/11/10

Task | Split | Progress | Milestone | Summary | Project Summary | External Tasks | External MileTask | Split

PDF created with pdfFactory Pro trial version www.software-partners.co.uk

ID	% Complete	Node	Projects	Task Name	Duration	Start	Finish
74	**100%**			**Area H2**	**44 days**	**Fri 30/07/10**	**Thu 30/09/10**
75	100%			Issue Contestable Charges to Distribution Customers	0 days	Fri 30/07/10	Fri 30/07/10
76	100%			Sub Group Response	22 days	Fri 30/07/10	Tue 31/08/10
77	100%			Issue Offers	22 days	Wed 01/09/10	Thu 30/09/10
78	**27%**			**Area H1**	**82 days**	**Mon 23/08/10**	**Wed 15/12/10**
79	100%			Issue Contestable Charges to Distribution Customers (Lisheen)	0 days	Mon 23/08/10	Mon 23/08/10
80	100%			Sub Group Response	22 days	Mon 23/08/10	Tue 21/09/10
81	0%			Issue Offers	60 days	Wed 22/09/10	Wed 15/12/10
82	**24%**			**Area H1**	**54 days**	**Thu 30/09/10**	**Wed 15/12/10**
83	60%			Issue Contestable Charges to Distribution Customers	0 days	Thu 30/09/10	Thu 30/09/10
84	60%			Sub Group Response	22 days	Fri 01/10/10	Tue 02/11/10
85	0%			Issue Offers	32 days	Tue 02/11/10	Wed 15/12/10
86	**36%**			**Area B [West Galway]**	**114 days**	**Tue 31/08/10**	**Fri 18/02/11**
87	100%			Issue Contestable Charges to Distribution Customers (West Galway)	19 days	Tue 31/08/10	Fri 24/09/10
88	100%			Sub Group Response	22 days	Mon 27/09/10	Wed 27/10/10
89	0%			Issue Offers	73 days	Thu 28/10/10	Fri 18/02/11
90	**13%**			**Area B [Bellacorrick]**	**89 days**	**Wed 06/10/10**	**Fri 18/02/11**
91	100%			Finalise Charging and Issue to Sub Group	12 days	Wed 06/10/10	Thu 21/10/10
92	0%			Sub Group Response	22 days	Fri 22/10/10	Mon 22/11/10
93	0%			Issue Offers	55 days	Tue 23/11/10	Fri 18/02/11
94	**0%**			**Area B**	**61 days**	**Mon 15/11/10**	**Fri 18/02/11**
95	0%			Finalise Charging and Issue to Sub Group	0 days	Mon 15/11/10	Mon 15/11/10
96	0%			Sub Group Response	22 days	Thu 18/11/10	Fri 17/12/10
97	0%			Issue Offers	32 days	Thu 06/01/11	Fri 18/02/11
98	**0%**			**Area F**	**58 days**	**Tue 30/11/10**	**Wed 02/03/11**
99	0%			Finalise Charging and Issue to Sub Group	0 days	Tue 30/11/10	Tue 30/11/10
100	0%			Sub Group Response	22 days	Wed 01/12/10	Wed 12/01/11
101	0%			Issue Offers	35 days	Thu 13/01/11	Wed 02/03/11
102	**0%**			**Area E**	**73 days**	**Mon 14/02/11**	**Mon 30/05/11**
103	0%			Finalise Charging and Issue to Sub Group	0 days	Mon 14/02/11	Mon 14/02/11
104	0%			Sub Group Response	22 days	Tue 15/02/11	Wed 16/03/11
105	0%			Issue Offers	50 days	Fri 18/03/11	Mon 30/05/11
106	**0%**			**Area E (TSO)**	**159 days**	**Wed 06/10/10**	**Wed 01/06/11**
107	0%			Finalise Charging and Issue to Sub Group (Cloghboola, Cordal, Kilgarvan)	19 days	Wed 06/10/10	Mon 01/11/10
108	0%			Sub Group Response	22 days	Tue 02/11/10	Wed 01/12/10
109	0%			Issue Offers	118 days	Thu 02/12/10	Wed 01/06/11
110	**0%**			**Area A (TSO)**	**140 days**	**Mon 29/11/10**	**Wed 29/06/11**
111	0%			Finalise Charging and Issue to Sub Group (Meenadreen)	20 days	Mon 29/11/10	Thu 06/01/11
112	0%			Sub Group Response	22 days	Fri 07/01/11	Mon 07/02/11
113	0%			Issue Offers	100 days	Fri 04/02/11	Wed 29/06/11
114	**0%**			**Area A**	**72 days**	**Wed 16/03/11**	**Wed 29/06/11**
115	0%			Finalise Charging and Issue to Sub Group	0 days	Wed 16/03/11	Wed 16/03/11
116	0%			Sub Group Response	22 days	Fri 18/03/11	Tue 19/04/11
117	0%			Issue Offers	49 days	Wed 20/04/11	Wed 29/06/11
118	**0%**			**Area J**	**73 days**	**Mon 14/02/11**	**Mon 30/05/11**
119	0%			Finalise Charging and Issue to Sub Group	0 days	Mon 14/02/11	Mon 14/02/11
120	0%			Sub Group Response	22 days	Tue 15/02/11	Wed 16/03/11
121	0%			Issue Offers	50 days	Fri 18/03/11	Mon 30/05/11
122	**0%**			**Area C**	**67 days**	**Thu 31/03/11**	**Wed 06/07/11**
123	0%			Finalise Charging and Issue to Sub Group	0 days	Thu 31/03/11	Thu 31/03/11
124	0%			Sub Group Response	22 days	Thu 31/03/11	Tue 03/05/11
125	0%			Issue Offers	45 days	Wed 04/05/11	Wed 06/07/11
126	**0%**			**Area G**	**53 days**	**Fri 29/04/11**	**Thu 14/07/11**
127	0%			Finalise Charging and Issue to Sub Group	0 days	Fri 29/04/11	Fri 29/04/11
128	0%			Sub Group Response	22 days	Tue 03/05/11	Wed 01/06/11
129	0%			Issue Offers	30 days	Thu 02/06/11	Thu 14/07/11
130	**0%**			**Area I**	**44 days**	**Mon 16/05/11**	**Fri 15/07/11**
131	0%			Finalise Charging and Issue to Sub Group	0 days	Mon 16/05/11	Mon 16/05/11
132	0%			Sub Group Response	22 days	Tue 17/05/11	Thu 16/06/11
133	0%			Issue Offers	22 days	Thu 16/06/11	Fri 15/07/11
134	**71%**			**TSO**	**741 days**	**Tue 15/07/08**	**Mon 18/07/11**
135	**100%**			**ITC**	**378 days**	**Tue 15/07/08**	**Thu 28/01/10**
136	**100%**			**ITC Preparation**	**139 days**	**Tue 15/07/08**	**Fri 06/02/09**
137	**100%**			**Agree Shallow Connection Nodes**	**126 days**	**Tue 15/07/08**	**Tue 20/01/09**
138	100%			DSO Produce wind database	4.4 wks	Tue 15/07/08	Wed 13/08/08
139	100%			TSO/DSO agree shallow connection nodes	2 days	Mon 19/01/09	Tue 20/01/09
140	100%			Publish shallow connection nodes	0 days	Tue 20/01/09	Tue 20/01/09
141	**100%**			**Prepare and Test ITC Inputs**	**10 days**	**Mon 26/01/09**	**Fri 06/02/09**
142	100%			Finalise ITC Input Files	10 days	Mon 26/01/09	Fri 06/02/09
143	**100%**			**ITC Execution**	**135 days**	**Mon 06/07/09**	**Tue 26/01/10**
144	100%			Run ITC from 2010 to 2025	135 days	Mon 06/07/09	Tue 26/01/10
145	**100%**			**ITC Technical Review**	**137 days**	**Mon 06/07/09**	**Thu 28/01/10**
146	100%			Have review carried out	137 days	Mon 06/07/09	Thu 28/01/10

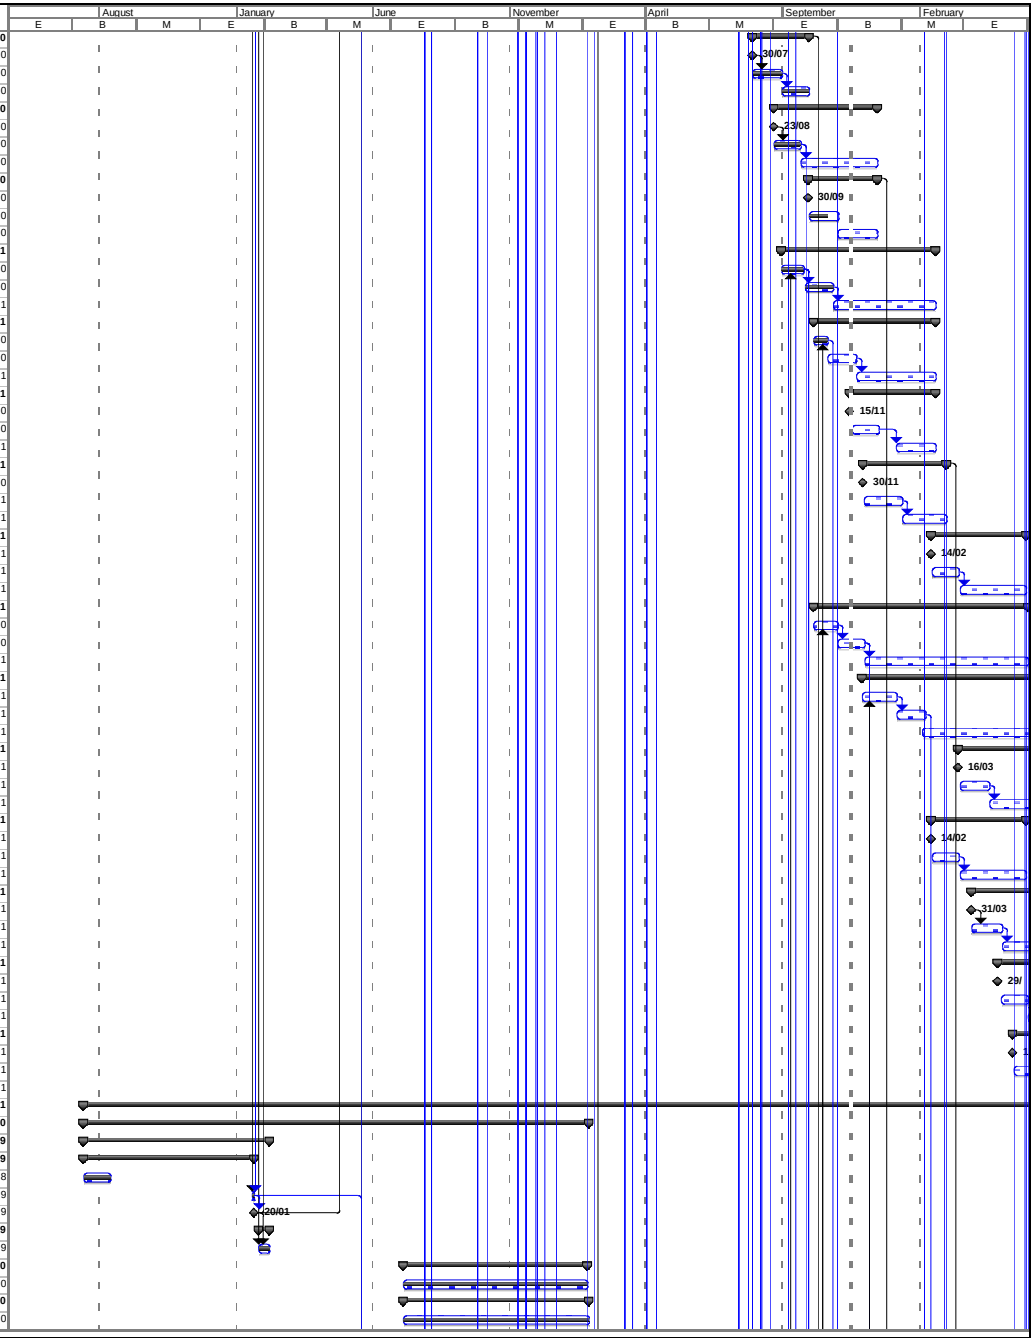

Project: Gate 3 Connection Offer Proces
Date: Mon 15/11/10

Task | Split | Progress | Milestone | Summary | Project Summary | External Tasks | External MileTask | Split

PDF created with pdfFactory Pro trial version www.software-partners.co.uk

ID	% Complete	Node	Projects	Task Name	Duration	Start	Finish
147	**69%**			**Offer Process**	**530 days**	**Mon 25/05/09**	**Mon 18/07/11**
148	**100%**			**Application checks**	**49 days**	**Mon 07/09/09**	**Fri 13/11/09**
149	100%			Area B	49 days	Mon 07/09/09	Fri 13/11/09
150	**100%**			**Initial Connection Method Dicussion Meetings**	**184 days**	**Mon 25/05/09**	**Mon 22/02/10**
151	**100%**			**Introductory Customer Meetings for Transmission Renewables**	**85 days**	**Mon 25/05/09**	**Mon 21/09/09**
152	100%			Area K	1 day	Mon 25/05/09	Mon 25/05/09
153	100%			Area D	1 day	Tue 02/06/09	Tue 02/06/09
154	100%			Area H2	1 day	Mon 22/06/09	Mon 22/06/09
155	100%			Area H1	1 day	Mon 29/06/09	Mon 29/06/09
156	100%			Area B	1 day	Thu 09/07/09	Thu 09/07/09
157	100%			Area E	1 day	Mon 27/07/09	Mon 27/07/09
158	100%			Area J	1 day	Mon 10/08/09	Mon 10/08/09
159	100%			Area F	1 day	Mon 24/08/09	Mon 24/08/09
160	100%			Area A	1 day	Mon 31/08/09	Mon 31/08/09
161	100%			Area G	1 day	Mon 07/09/09	Mon 07/09/09
162	100%			Area C	1 day	Mon 14/09/09	Mon 14/09/09
163	100%			Area I	1 day	Mon 21/09/09	Mon 21/09/09
164	100%			Initial Connection Leadtimes for Constraints Analysis	0 days	Fri 10/07/09	Fri 10/07/09
165	100%			Leadtimes for offers agreed with DSO	17 days	Fri 29/01/10	Mon 22/02/10
166	**100%**			**Publish Offer Leadtimes and Firm Access Quantities**	**20 days**	**Fri 18/12/09**	**Fri 29/01/10**
167	100%			2010-2017	0 days	Fri 18/12/09	Fri 18/12/09
168	100%			2018-2021	0 days	Wed 20/01/10	Wed 20/01/10
169	100%			2021-2025	0 days	Fri 29/01/10	Fri 29/01/10
170	**67%**			**Application Fees**	**295 days**	**Fri 16/10/09**	**Fri 07/01/11**
171	100%			Invoice fees for offers due to issue in 2009	5 days	Fri 16/10/09	Thu 22/10/09
172	100%			Invoice fees for offers due to issue in 2010	5 days	Mon 04/01/10	Fri 08/01/10
173	0%			Invoice fees for offers due to issue in 2011	5 days	Mon 03/01/11	Fri 07/01/11
174	**73%**			**Prepare and Issue Offers [CER-08-260]**	**458 days**	**Tue 04/08/09**	**Thu 16/06/11**
175	**100%**			**Area K**	**82 days**	**Tue 04/08/09**	**Thu 26/11/09**
176	100%			DSO	82 days	Tue 04/08/09	Thu 26/11/09
177	100%			TSO	81 days	Tue 04/08/09	Wed 25/11/09
178	**100%**			**Area D**	**99 days**	**Fri 02/10/09**	**Thu 04/03/10**
179	100%			DSO	99 days	Fri 02/10/09	Thu 04/03/10
180	**100%**			**Area H2**	**155 days**	**Mon 07/12/09**	**Thu 29/07/10**
181	100%			DSO	130 days	Mon 07/12/09	Thu 24/06/10
182	100%			TSO	155 days	Mon 07/12/09	Thu 29/07/10
183	**100%**			**Area H1**	**198 days**	**Wed 25/11/09**	**Fri 17/09/10**
184	100%			DSO	168 days	Wed 25/11/09	Fri 06/08/10
185	100%			TSO	198 days	Wed 25/11/09	Fri 17/09/10
186	**100%**			**Area B**	**222 days**	**Mon 16/11/09**	**Wed 13/10/10**
187	100%			DSO	192 days	Mon 16/11/09	Tue 31/08/10
188	100%			TSO	222 days	Mon 16/11/09	Wed 13/10/10
189	**100%**			**Area F**	**160 days**	**Thu 08/04/10**	**Tue 23/11/10**
190	100%			DSO	140 days	Thu 08/04/10	Tue 26/10/10
191	100%			TSO	160 days	Thu 08/04/10	Tue 23/11/10
192	**78%**			**Area E**	**240 days**	**Mon 15/03/10**	**Fri 04/03/11**
193	87%			DSO	195 days	Mon 15/03/10	Mon 03/01/11
194	71%			TSO	240 days	Mon 15/03/10	Fri 04/03/11
195	**66%**			**Area J**	**249 days**	**Thu 08/04/10**	**Tue 12/04/11**
196	70%			DSO	219 days	Thu 08/04/10	Fri 25/02/11
197	62%			TSO	249 days	Thu 08/04/10	Tue 12/04/11
198	**41%**			**Area A**	**218 days**	**Tue 20/07/10**	**Thu 09/06/11**
199	44%			DSO	188 days	Tue 20/07/10	Tue 26/04/11
200	38%			TSO	218 days	Tue 20/07/10	Thu 09/06/11
201	**36%**			**Area G**	**181 days**	**Fri 13/08/10**	**Wed 11/05/11**
202	36%			DSO	181 days	Fri 13/08/10	Wed 11/05/11
203	**36%**			**Area C**	**213 days**	**Wed 04/08/10**	**Thu 16/06/11**
204	37%			DSO	196 days	Wed 04/08/10	Mon 23/05/11
205	34%			TSO	213 days	Wed 04/08/10	Thu 16/06/11
206	**26%**			**Area I**	**173 days**	**Mon 13/09/10**	**Mon 30/05/11**
207	26%			DSO	173 days	Mon 13/09/10	Mon 30/05/11
208	**18%**			**Prepare and Issue Offers [CER 10/056]**	**210 days**	**Fri 23/07/10**	**Wed 01/06/11**
209	**100%**			**Area H1**	**59 days**	**Fri 23/07/10**	**Fri 15/10/10**
210	100%			Issue Contestable Charges to DSO	0 days	Fri 23/07/10	Fri 23/07/10
211	100%			Sub Group Reponse on Contestability (Bruckana at Lisheen 110kV Station)	0 days	Tue 21/09/10	Tue 21/09/10
212	**100%**			**Prepare and Issue Offers**	**17 days**	**Wed 22/09/10**	**Fri 15/10/10**
213	100%			DSO	17 days	Wed 22/09/10	Fri 15/10/10
214	**39%**			**Area B [West Galway]**	**114 days**	**Tue 31/08/10**	**Fri 18/02/11**
215	100%			Issue Contestable Charges to DSO (West Galway)	0 days	Tue 31/08/10	Tue 31/08/10
216	100%			Issue Contestable Charges to Transmission Customers (West Galway)	0 days	Fri 24/09/10	Fri 24/09/10
217	100%			Sub Group Reponse on Contestability	22 days	Mon 27/09/10	Wed 27/10/10
218	**26%**			**Issue Offers**	**73 days**	**Thu 28/10/10**	**Fri 18/02/11**
219	48%			DSO	27 days	Thu 28/10/10	Fri 03/12/10

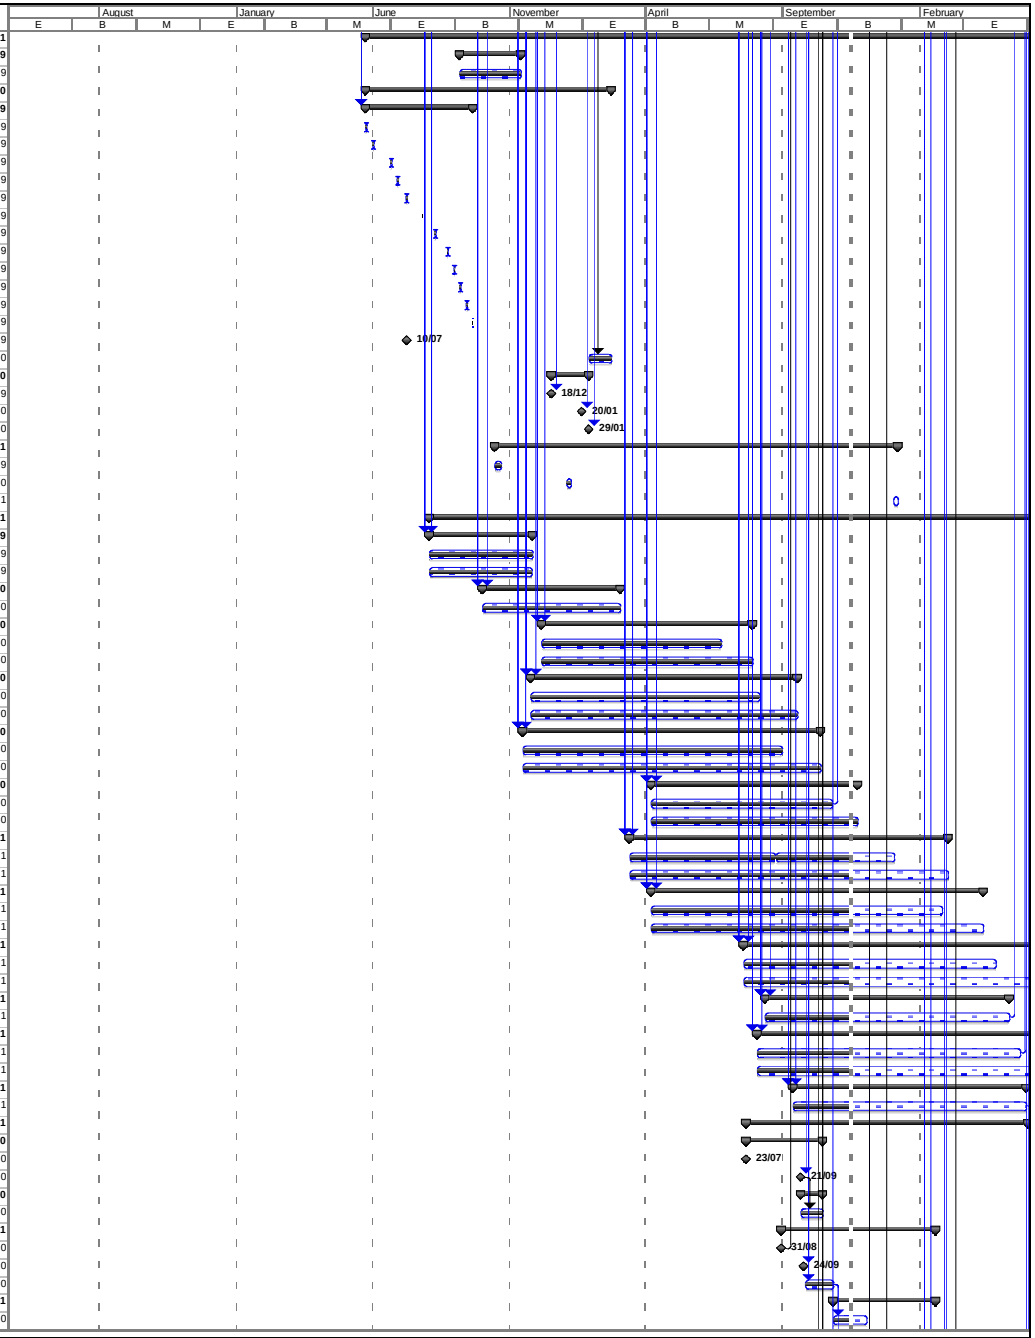

Project: Gate 3 Connection Offer Proces
Date: Mon 15/11/10

Task | Split | Progress | Milestone | Summary | Project Summary | External Tasks | External MileTask | Split

PDF created with pdfFactory Pro trial version www.software-partners.co.uk

ID	% Complete	Node	Projects	Task Name	Duration	Start	Finish
220	18%			TSO	73 days	Thu 28/10/10	Fri 18/02/11
221	**18%**			**Area B [Bellacorrick]**	**89 days**	**Wed 06/10/10**	**Fri 18/02/11**
222	100%			Issue Contestable Charges to DSO (Bellacorick)	0 days	Wed 06/10/10	Wed 06/10/10
223	100%			Issue Contestable Charges to Transmission Cstomers (Bellacorick)	0 days	Thu 21/10/10	Thu 21/10/10
224	77%			Sub Group Reponse on Contestability (Bellacorick)	22 days	Fri 22/10/10	Mon 22/11/10
225	**0%**			**Issue Offers**	**55 days**	**Tue 23/11/10**	**Fri 18/02/11**
226	0%			DSO	19 days	Tue 23/11/10	Fri 17/12/10
227	0%			TSO	55 days	Tue 23/11/10	Fri 18/02/11
228	**0%**			**Area E**	**159 days**	**Wed 06/10/10**	**Wed 01/06/11**
229	100%			Issue Contestable Charges to DSO	0 days	Wed 06/10/10	Wed 06/10/10
230	0%			Sub Group Reponse on Contestability (Area E)	0 days	Wed 01/12/10	Wed 01/12/10
231	**0%**			**Issue Offers**	**118 days**	**Thu 02/12/10**	**Wed 01/06/11**
232	0%			DSO	43 days	Thu 02/12/10	Fri 11/02/11
233	0%			TSO	118 days	Thu 02/12/10	Wed 01/06/11
234	**0%**			**Area A**	**98 days**	**Fri 26/11/10**	**Thu 28/04/11**
235	0%			Issue Contestable Charges to DSO	0 days	Fri 26/11/10	Fri 26/11/10
236	0%			Sub Group Response on Contestability	0 days	Mon 07/02/11	Mon 07/02/11
237	**0%**			**Issue Offers**	**56 days**	**Tue 08/02/11**	**Thu 28/04/11**
238	0%			DSO	56 days	Tue 08/02/11	Thu 28/04/11
239	**89%**			**Constraints Information**	**460 days**	**Tue 01/09/09**	**Mon 18/07/11**
240	100%			Perform Constraint Studies	243 days	Tue 01/09/09	Fri 27/08/10
241	**75%**			**PGOR Reports**	**63 days**	**Mon 20/09/10**	**Thu 16/12/10**
242	100%			Reports Available for Region K	1 day	Mon 20/09/10	Mon 20/09/10
243	100%			Reports Available for Region D	1 day	Mon 20/09/10	Mon 20/09/10
244	100%			Reports Available for Region H2	1 day	Fri 01/10/10	Fri 01/10/10
245	0%			Reports Available for Area H1	1 day	Thu 16/12/10	Thu 16/12/10
246	**0%**			**Constraint Reports**	**116 days**	**Tue 01/02/11**	**Mon 18/07/11**
247	0%			Impact Assessment of Scheduling and Dispatch Paper	20 days	Tue 01/02/11	Mon 28/02/11
248	0%			Report Available for Region K, D, H2, H1 & B	1 day	Tue 01/03/11	Tue 01/03/11
249	0%			Report Available for Region F	1 day	Thu 03/03/11	Thu 03/03/11
250	0%			Report Available for Region E	1 day	Thu 02/06/11	Thu 02/06/11
251	0%			Report Available for Region J	1 day	Tue 31/05/11	Tue 31/05/11
252	0%			Report Available for Region A	1 day	Thu 30/06/11	Thu 30/06/11
253	0%			Report Available for Region G	1 day	Fri 15/07/11	Fri 15/07/11
254	0%			Report Available for Region C	1 day	Thu 07/07/11	Thu 07/07/11
255	0%			Report Available for Region I	1 day	Mon 18/07/11	Mon 18/07/11

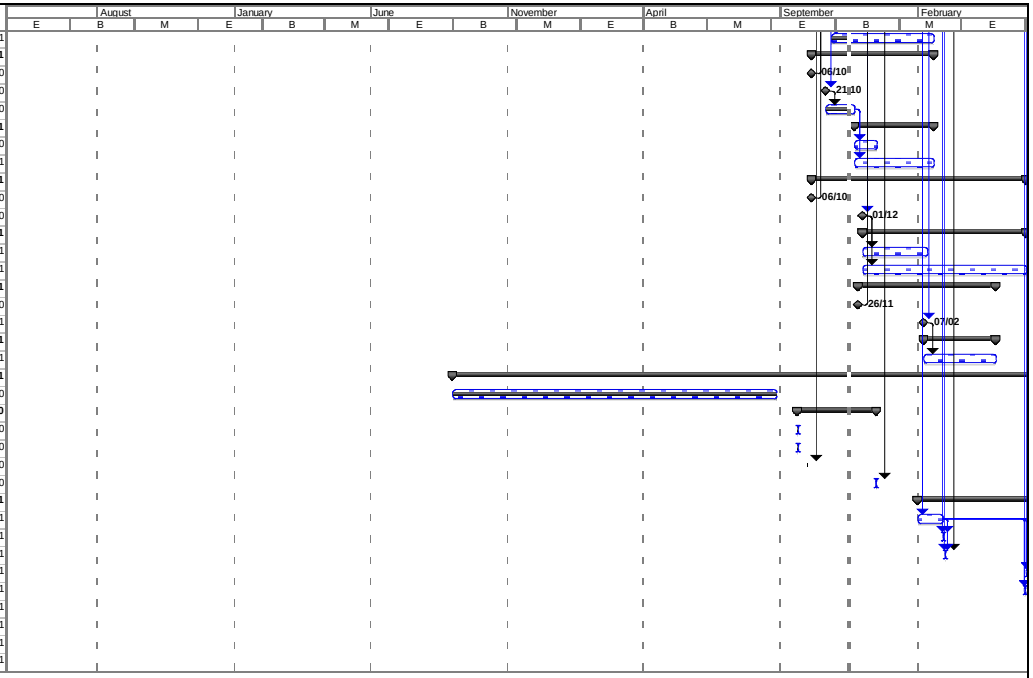

Project: Gate 3 Connection Offer Proces
Date: Mon 15/11/10

Task | Split | Progress | Milestone | Summary | Project Summary | External Tasks | External MileTask | Split

PDF created with pdfFactory Pro trial version www.software-partners.co.uk
